


9/12/2006

Overall:

- Working with BoR to property tag and pay newly received equipment
- BellSouth has delivered 5 of the 10 outstanding local loops
- SU working on purchasing and installing UPS for P5
- Completed network equipment setup at UNO
- UNO P5 move on August 29<sup>th</sup>
- ULL P5 delivered and network configured
- Completed fiber characterization between Baton Rouge and LaPlace on Qwest/DOTD fiber
- Moved LSU, UNO and PBMR to 500Meg Internet service out of Baton Rouge
- Working on interconnect order between Qwest and BellSouth
- Completed on Letter of Agency from DOTD to Qwest
- Working on I-20 colocation
- Working on Jackson to Baton Rouge colocation
- Completed on fiber repairs from Monroe and Ruston
- Completed network equipment setup at LSU HSC N.O.
- Completed staging and pre-configuration for Hwy. 90 route
- Working on finishing staging and pre-configuration for Jackson to Baton Rouge route
- Franklin site to be installed 9/20 and Schriever on 9/21
- Jackson,MS local loop dark fiber rebid

Issues:

- Sun America IRU
- Interconnect order between Qwest and BellSouth
- McLeodUSA collocation contract
- AUP with BellSouth
- BellSouth IRU on Hwy.90 fiber to Qwest
- Missing local loop dark fiber routes
- Missing conduit at Lafayette Qwest location
- Signed CEA with DOTD

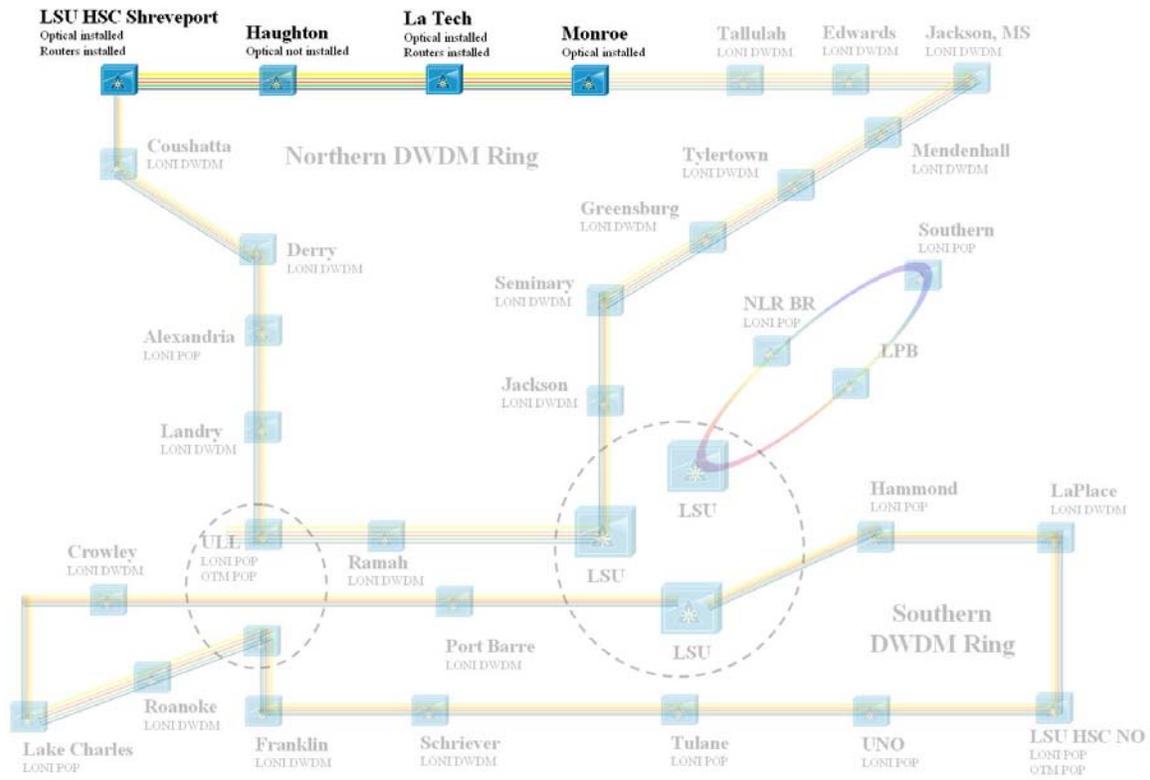

9/12/2006

Shreveport to Monroe:

Completed

HSC Shreveport Optical and Routers Installation

La Tech Optical and Routers Installation

Monroe Optical Installation

La Tech P5 Installation

Cisco Equipment Ordered (DCUs only)

Move La Tech P5 to Internet2

BellSouth Local Loop to La Tech

Cisco Equipment Order

Pending


Signed CEA

Fiber Characterization

BellSouth Local Loop in Shreveport has no completion date but construction has started

BellSouth Local Loop in Monroe has no completion date but testing as started

Haughton Optical Installation

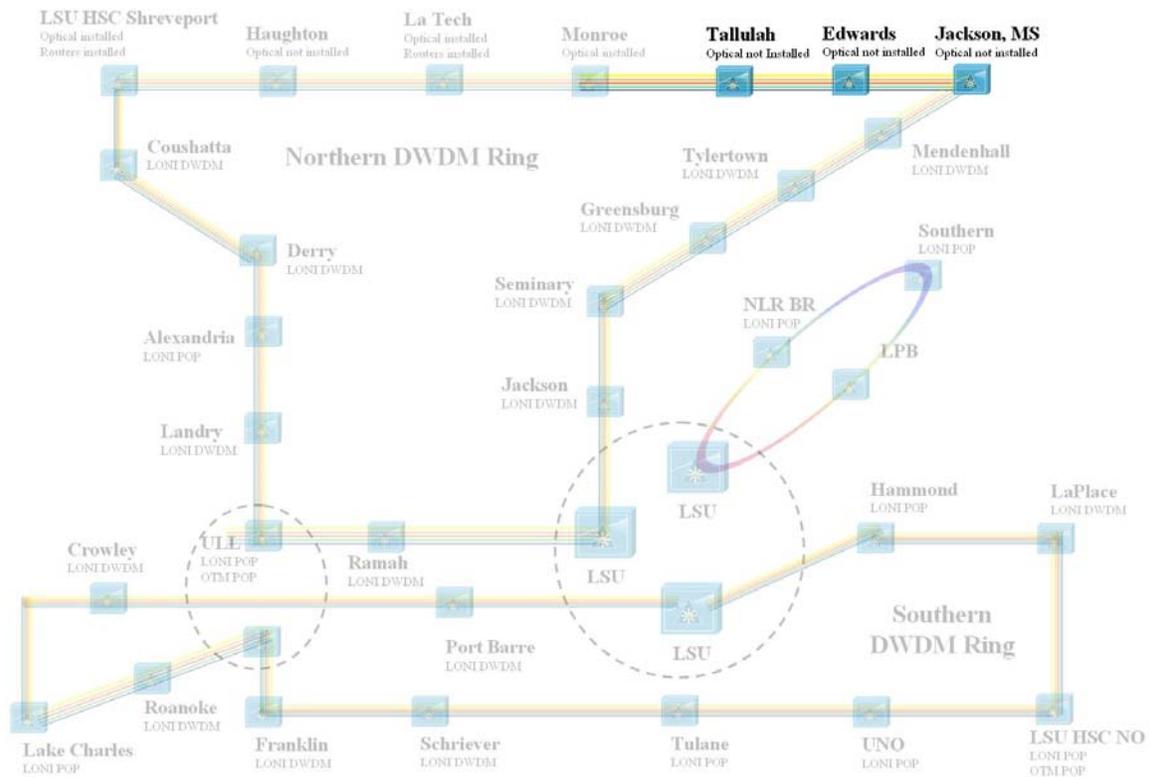

9/12/2006


Monroe to Jackson, MS:

Completed

Award of route to ITC^DeltaCom and fiber assignment  
 Site Survey of the Route  
 Cisco Equipment Order

Pending

Fiber Assignments  
 Fiber Characterization  
 BellSouth Local Loop in Monroe has no completion date but testing as started  
 Tallulah Optical Installation  
 Edwards Optical Installation  
 Jackson, MS Optical Installation  
 Jackson, MS Local Loop rebid

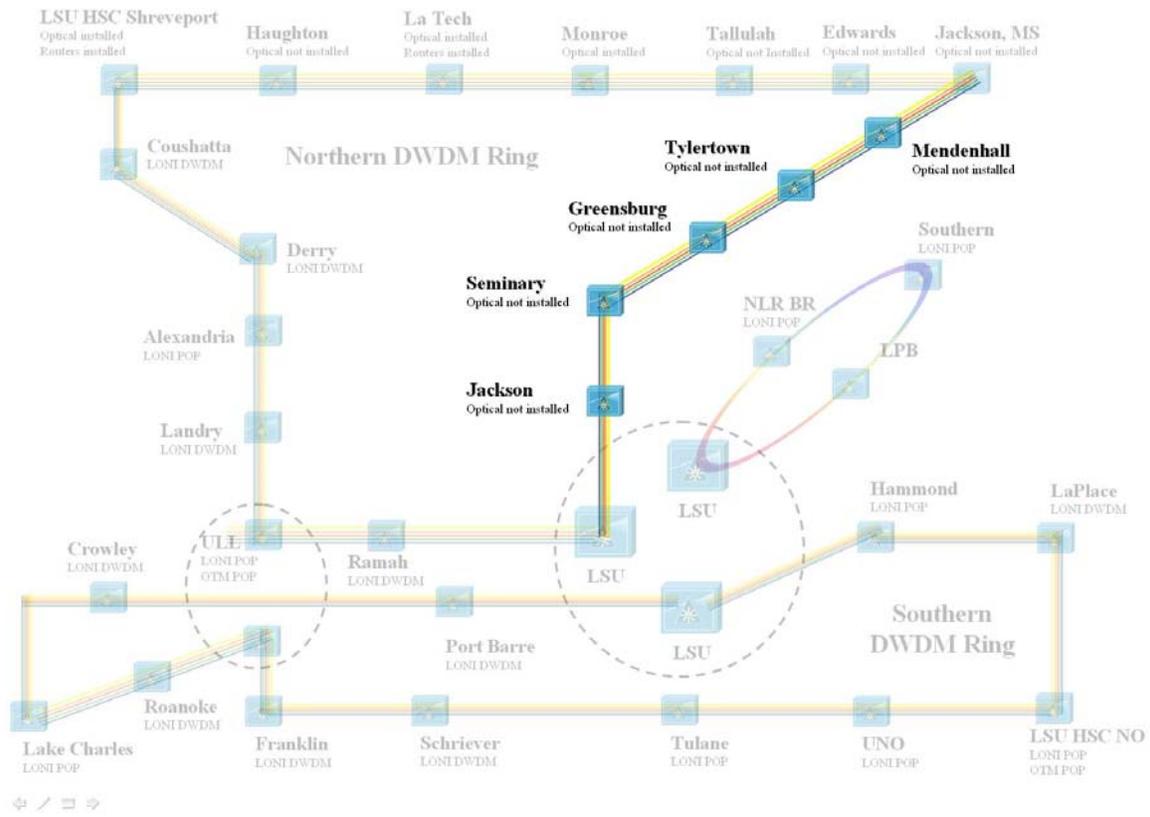

9/12/2006


Jackson, MS to Baton Rouge:

Completed

Award of Route to WilTel/Level3  
 Cisco Equipment Ordered  
 WilTel/Level3 Kick-off

Pending

Site Survey of the Route  
 Fiber Assignments  
 Fiber Characterization  
 Mendenhall, MS Optical Installation  
 Tylertown, MS Optical Installation  
 Greensburg, MS Optical Installation  
 Seminary, MS Optical Installation  
 Jackson, LA Optical Installation  
 L Band DCUs from Cisco/BellSouth

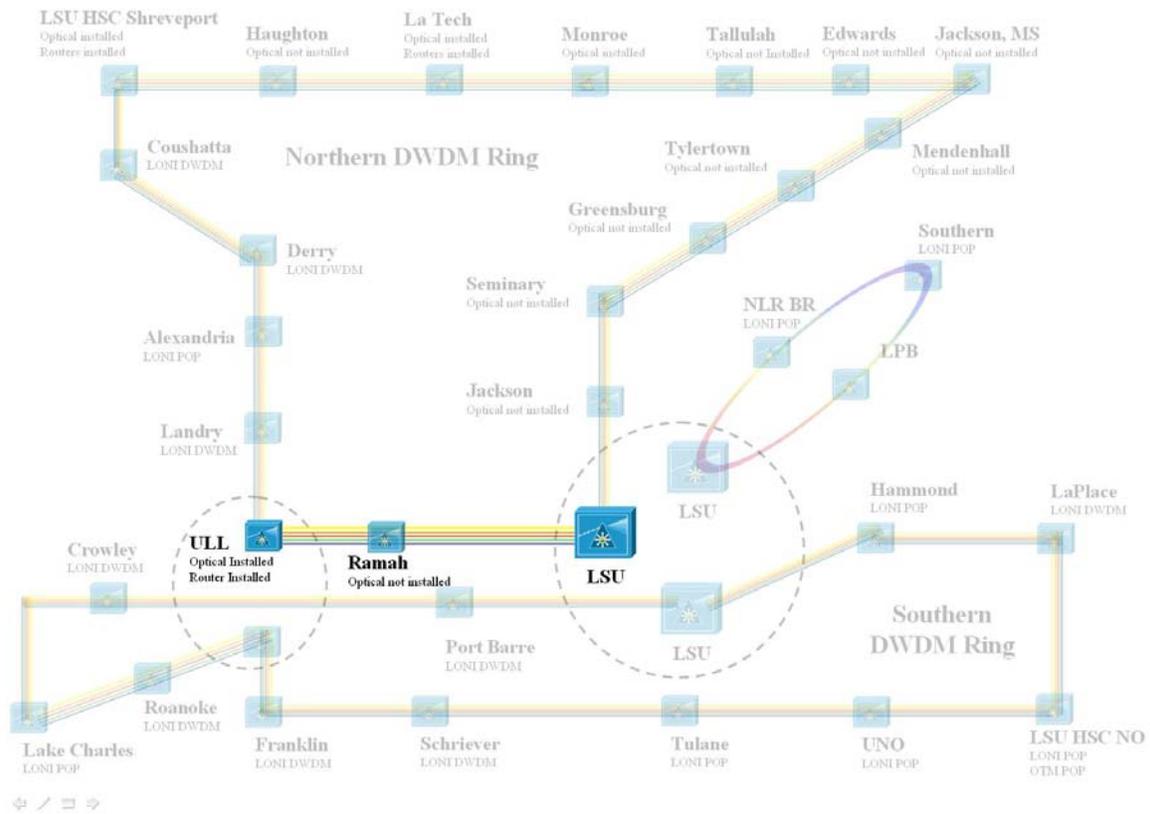

9/12/2006


Baton Rouge to Lafayette:

Completed

- LSU Optical and Routers Installation
- ULL Optical and Routers Installation at Abdalla
- ULL Optical Installation at Stephens
- Cisco Equipment Ordered
- ULL P5 delivered and network completed
- Ramah Optical Installation
- Fiber Characterization complete from Ramah to Baton Rouge
- Route Construction for DOTD/Qwest
- ULL P5 Installation

Pending

- Signed CEA
- Qwest access and conduit in Lafayette
- BellSouth and Qwest interconnect in Lafayette

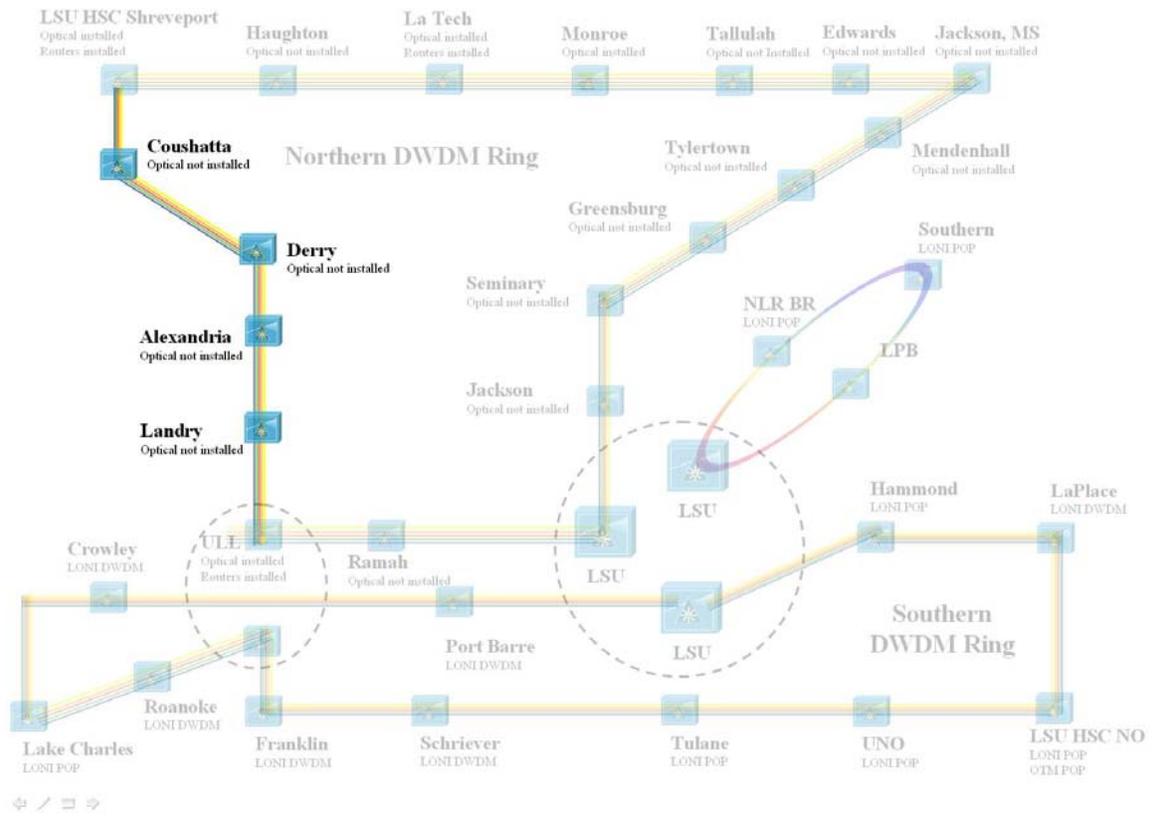

9/12/2006


Lafayette to Shreveport:

Completed

Award route to Sun America  
Cisco Equipment Ordered (DCUs only)

Pending

Signed CEA  
IRU with Sun America  
Site Survey of the Route  
Fiber Assignments  
Fiber Characterization  
Landry Optical Installation  
Alexandria Optical Installation  
Derry Optical Installation  
Coushatta Optical Installation

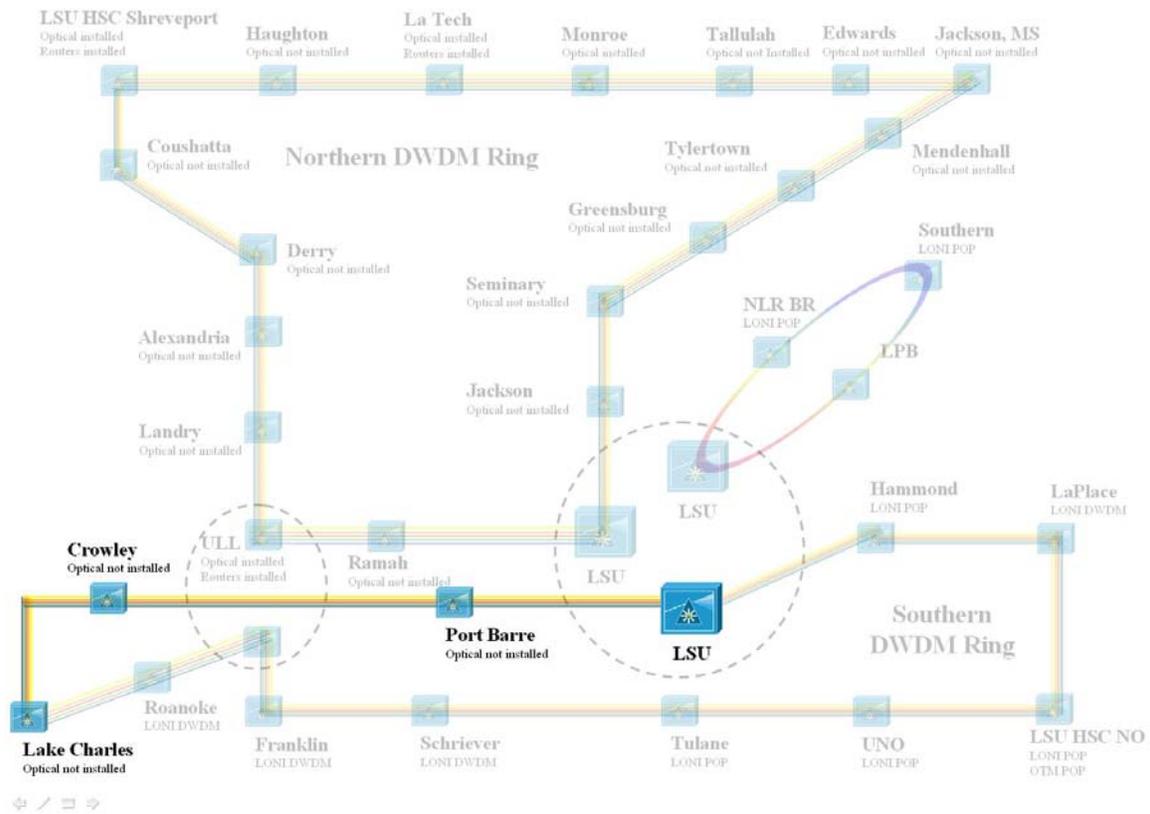

9/12/2006

Lake Charles to Baton Rouge:

Completed

Utilize AT&T Fiber

LSU Optical and Routers Installation

Pending

Route Construction by AT&T

Site Survey of the Route

Fiber Assignments

Fiber Characterization


Lake Charles Optical and Routers Installation

Crowley Optical Installation

Port Barre Optical Installation

Cisco Equipment Order for LPB

BellSouth Local Loop from McNeese to AT&T PoP and LSU to AT&T PoP respectively

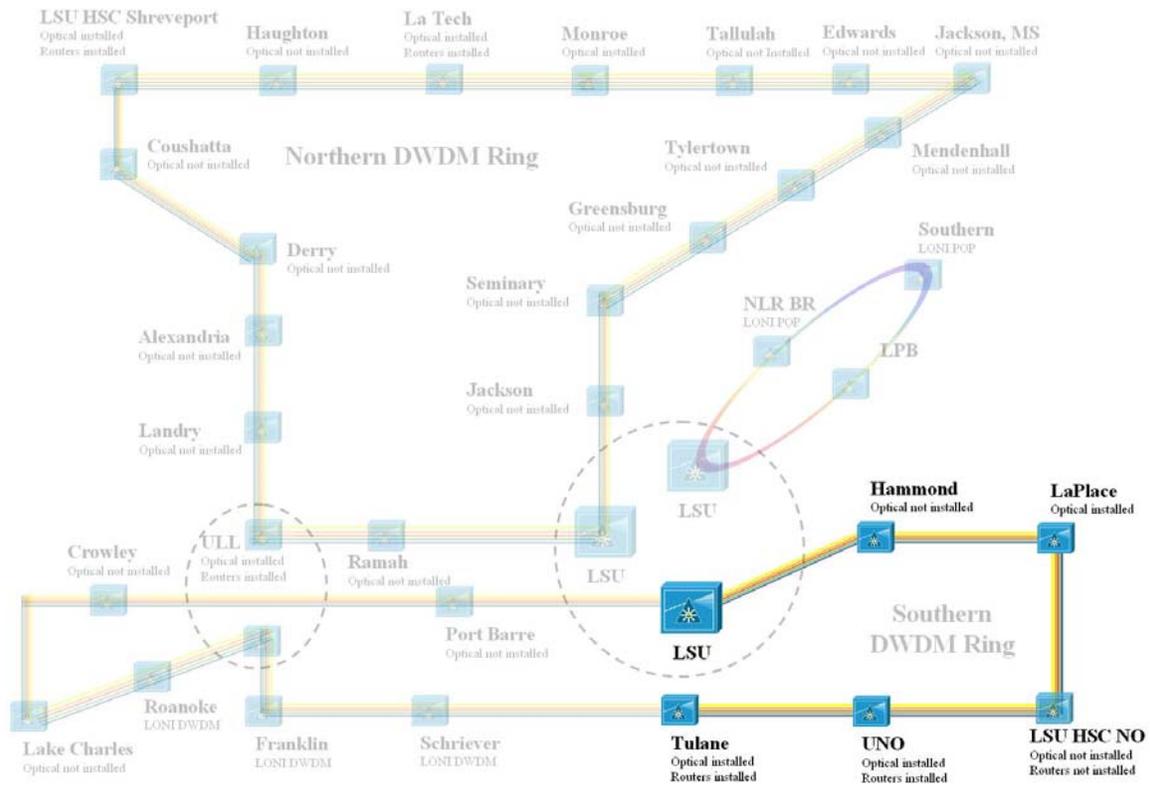

9/12/2006


Baton Rouge to New Orleans:

Completed

- LSU Optical and Routers Installation
- LaPlace Optical Installation
- Baton Rouge to LaPlace Fiber is Lit
- UNO Optical and Routers Installation
- Tulane Optical and Routers Installation
- LSU HSC Optical and Routers Installation
- Tulane P5 Installation
- UNO P5 Installation
- Cisco Equipment Order
- Route Construction for DOTD/Qwest

Pending

- Signed CEA
- BellSouth and Qwest interconnect in New Orleans
- BellSouth Local Loop in New Orleans between UNO and Tulane has no completion date

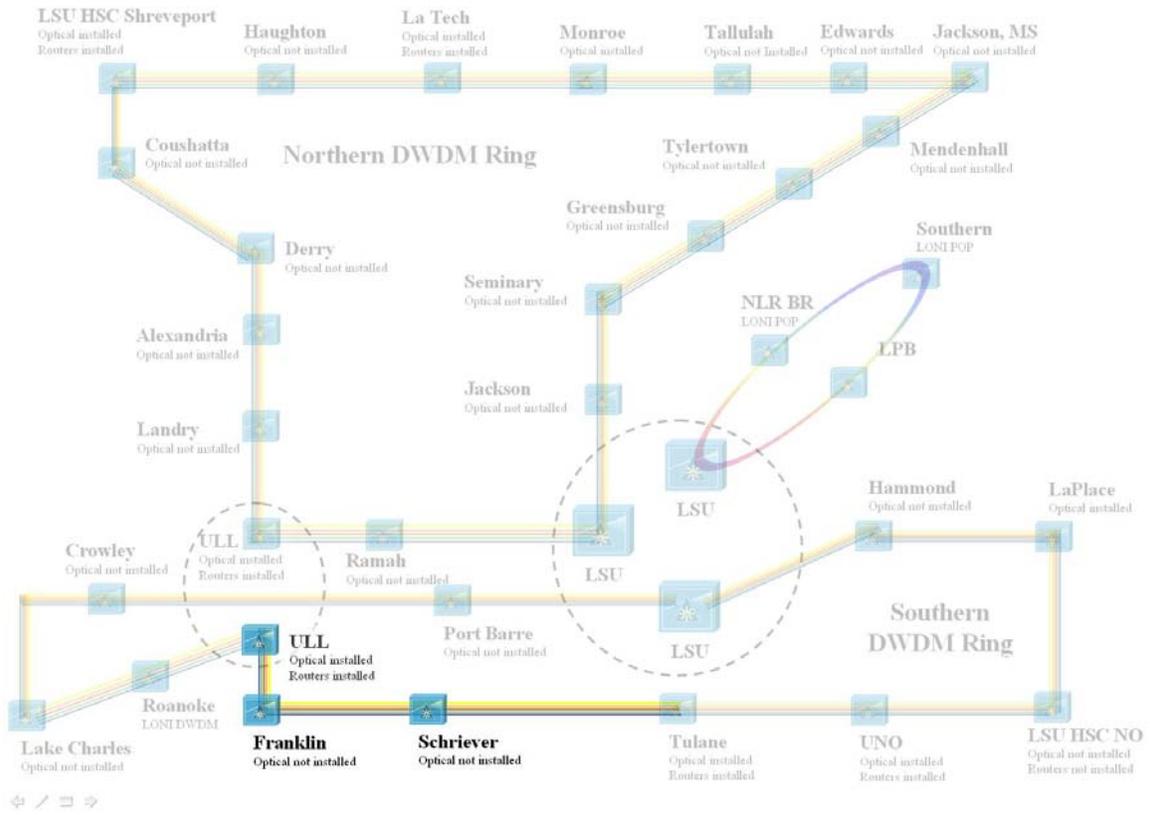

9/12/2006


New Orleans to Lafayette:

Completed

Award of Route to BellSouth  
Cisco Equipment Order

Pending

IRU with BellSouth  
Site Survey of the Route  
Fiber Assignments  
Fiber Characterization  
BellSouth Local Loop to ULL has no completion date but testing as started  
Schriever Optical Installation  
Franklin Optical Installation

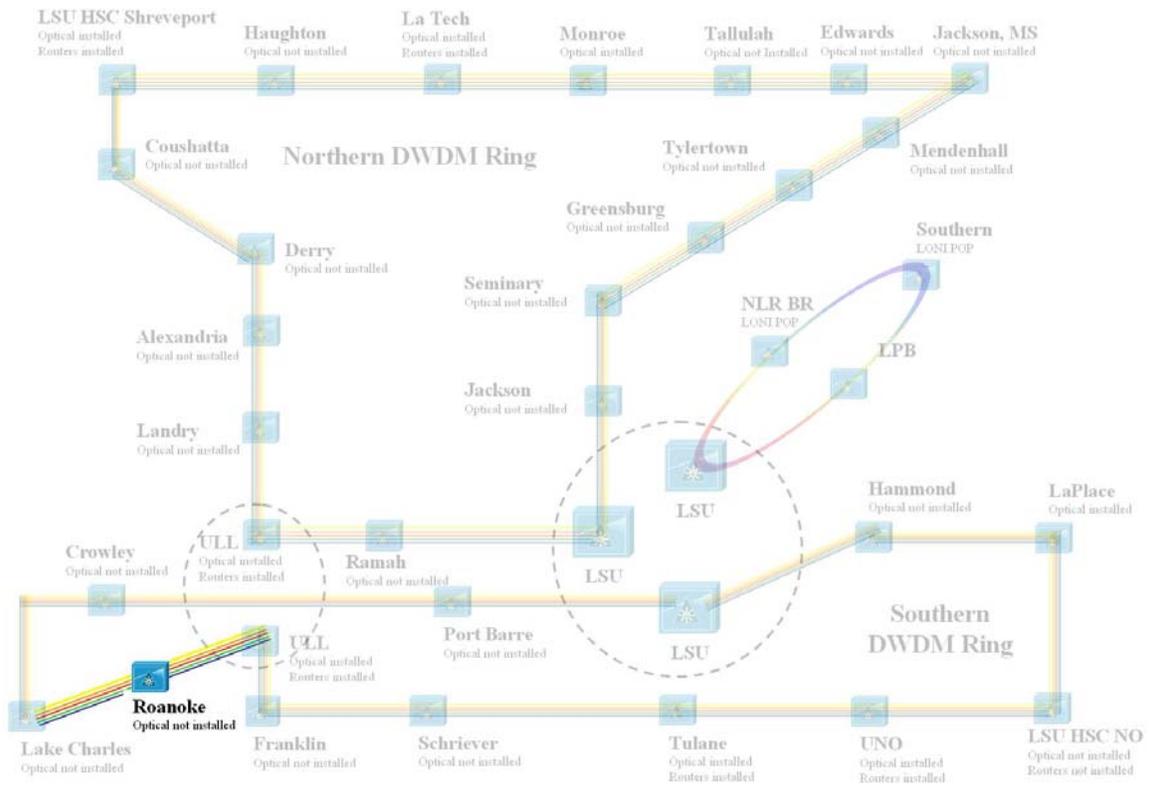

9/12/2006

Lafayette to Lake Charles:

Completed

Route Construction for DOTD/Qwest

Pending

Signed CEA

Site Survey of the Route


Fiber Assignments

Fiber Characterization

Cisco Equipment Order for LPB

Roanoke Optical Installation

BellSouth Local Loop McNeese has no completion date

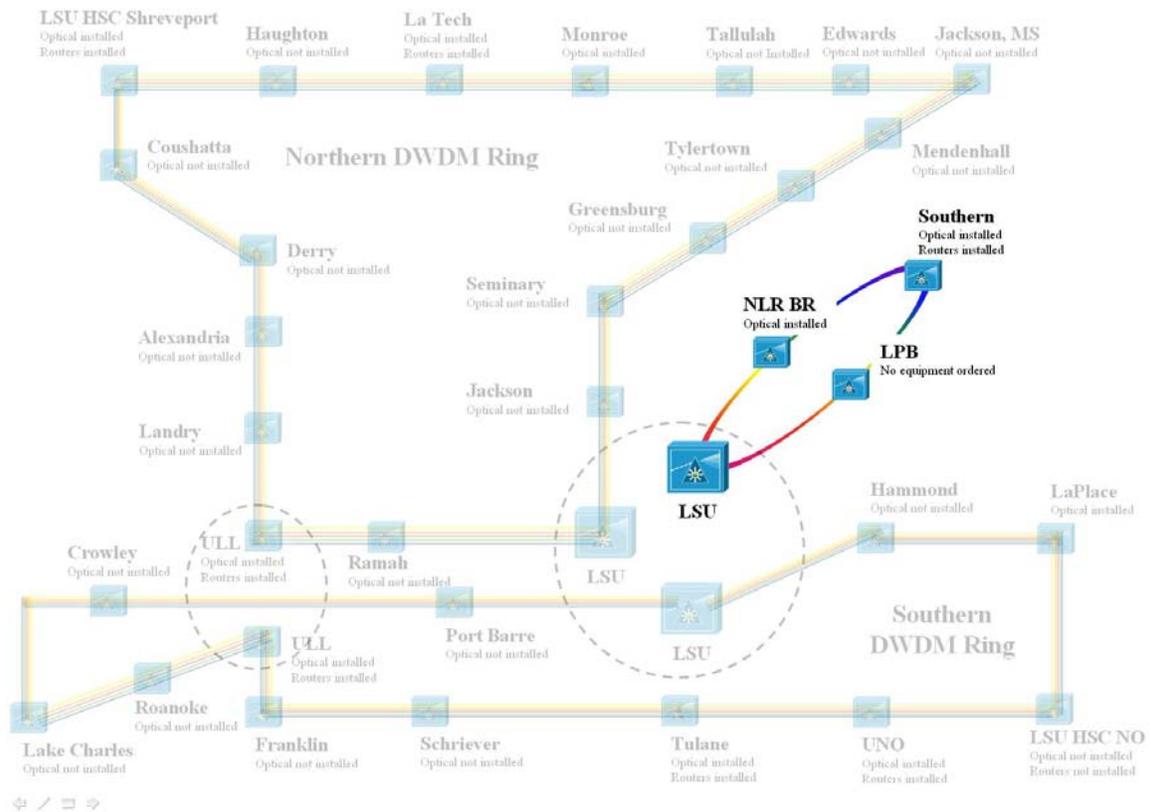

9/12/2006

Baton Rouge Ring:  
Completed

- LSU Optical and Routers Installation
- NLR Optical Installation
- SU Optical and Routers Installation
- Cisco Equipment Order
- (4) 10GE Circuits from LSU to SU
- (1) 10GE Circuit to NLR
- (1) 1GE Circuit to NLR

Pending

- Fiber Characterization
- BellSouth Loop Local from SU to WilTel/Level3 to complete the metro ring has no completion date
- SU UPS Installation
- SU P5 Installation
- Cisco Equipment Order for LPB
