

8/09/2006


Overall:

- All remaining Cisco equipment should arrive by August 15th
- BellSouth is still working delivering local loops
- SU working on purchasing and installing UPS for P5
- Schedule UNO P5 move on August 28th
- ULL P5 delivered and network configured
- Move Tech P5 to Internet2 connection
- Completed fiber characterization between Baton Rouge and Lafayette on Qwest/DOTD fiber
- Targeting LONI peerings with LSU and SU by August 28th
- Working on interconnect order between Qwest and BellSouth
- Working on Letter of Agency from DOTD to Qwest
- Working on Letter of Agency from BellSouth to Qwest
- Working on I-20 colocation
- Working on Jackson to Baton Rouge colocation
- Working on repairing splice in Monroe and Ruston
- Working on inventory for Risk Management
- Working on powering-up UNO network equipment next week
- Working on powering-up LSU HSC N.O. network equipment next week
- Working on finishing staging and pre-configuration for rest of equipment
- Working on gaining access to Qwest sites in Schriever and Franklin

- Jackson,MS local loop dark fiber rebid
- Working on conduit at WilTel/Level3 PoP

Issues:

- Sun America IRU
- Letter of Agency from DOTD to Qwest
- Letter of Agency from BellSouth to Qwest
- Interconnect order between Qwest and BellSouth
- McLeodUSA colocation
- WilTel/Level3 colocation
- AUP with BellSouth
- BellSouth IRU on Hwy.90 fiber to Qwest
- Missing local loop dark fiber routes
- Missing conduit at WilTel/Level3 PoP

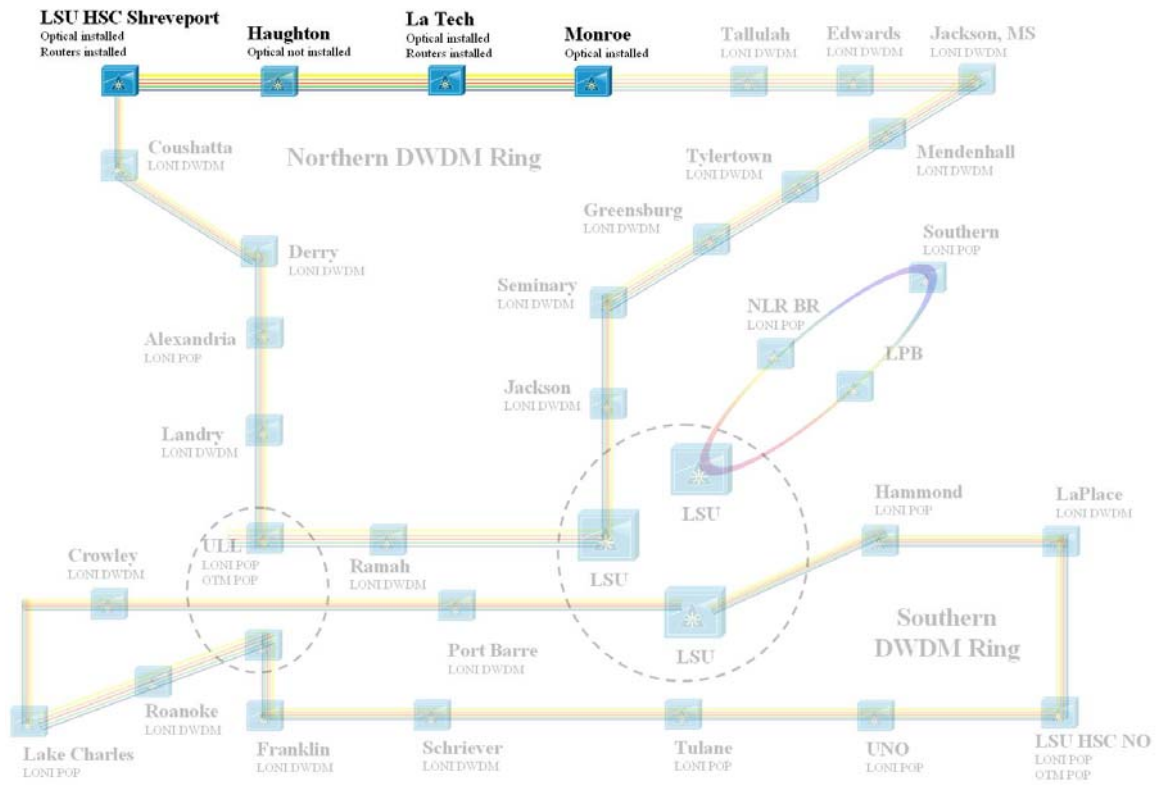

8/09/2006

Shreveport to Monroe:

Completed

HSC Shreveport Optical and Routers Installation

La Tech Optical and Routers Installation

Monroe Optical Installation

La Tech P5 Installation

Cisco Equipment Ordered (DCUs only)

Move La Tech P5 to Internet2

Pending

CEA

Fiber Characterization

BellSouth Local Loop in Shreveport has no completion date

BellSouth Local Loop in Ruston planned has no completion date


BellSouth Local Loop in Monroe has no completion date

Cisco Equipment Delivery (DCUs only) scheduled to arrive by August

15th

Haughton Optical Installation

No responses to the Dark Fiber Bid opens June 20th

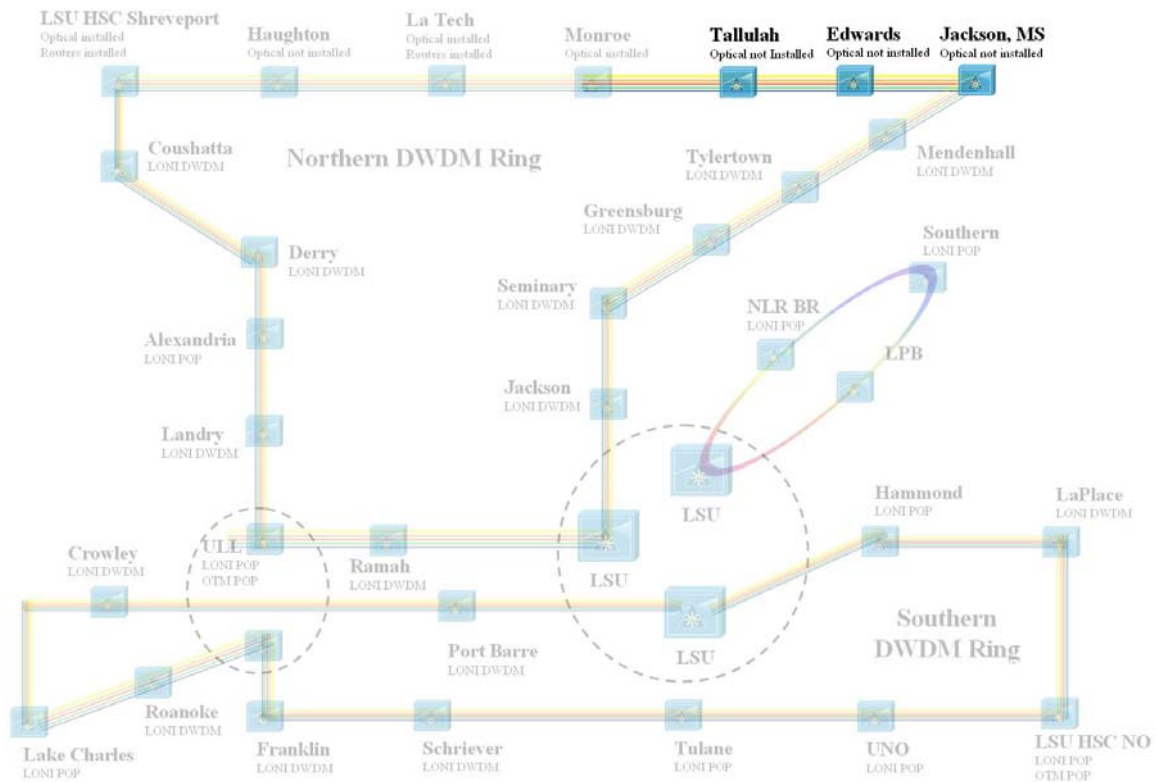

8/09/2006


Monroe to Jackson, MS:

Completed

Award of route to ITC^DeltaCom
 Site Survey of the Route
 Cisco Equipment Ordered

Pending

Fiber Assignments
 Fiber Characterization
 BellSouth Local Loop in Monroe has no completion date
 Cisco Equipment Delivery scheduled to arrive by July August 15th
 Tallulah Optical Installation
 Edwards Optical Installation
 Jackson, MS Optical Installation
 Jackson, MS Local Loop rebid

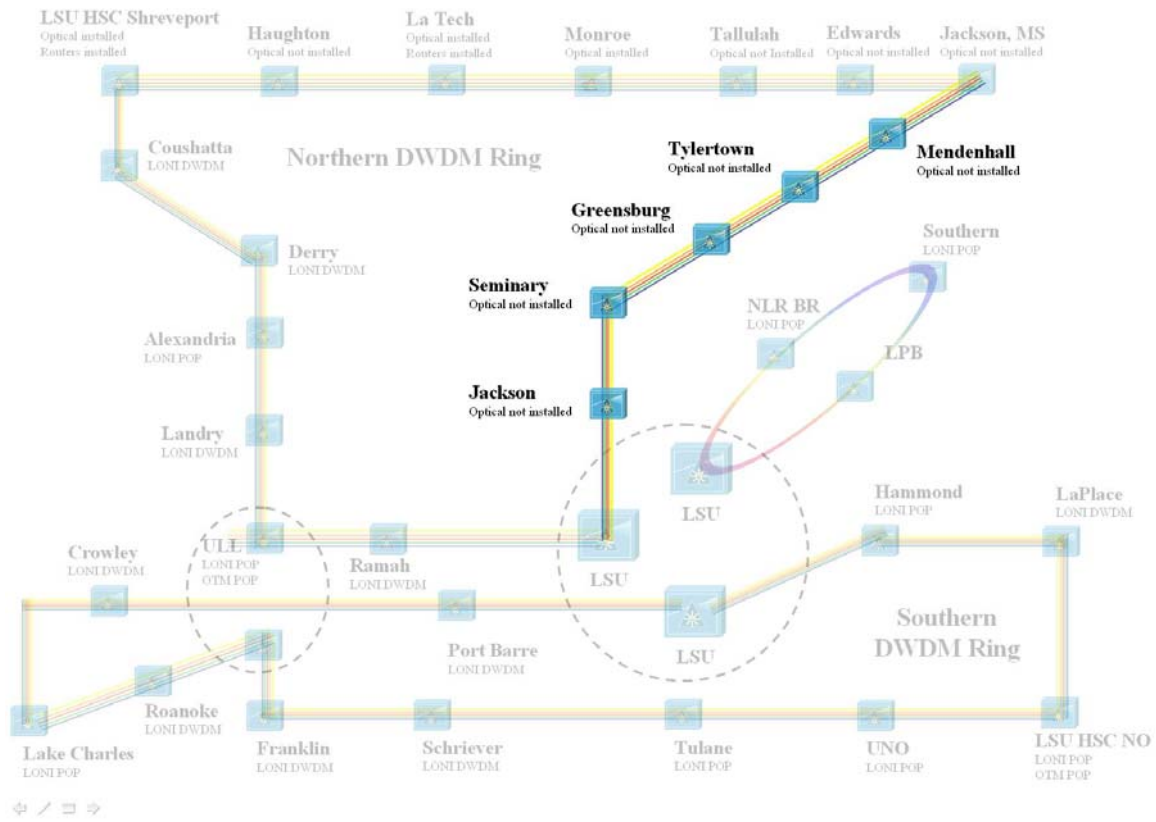

8/09/2006


Jackson, MS to Baton Rouge:

Completed

Award of Route to WilTel/Level3
 Cisco Equipment Ordered
 WilTel/Level3 Kick-off

Pending

Site Survey of the Route
 Fiber Assignments
 Fiber Characterization
 Cisco Equipment Delivery scheduled to arrive by August 15th
 Mendenhall, MS Optical Installation
 Tylertown, MS Optical Installation
 Greensburg, MS Optical Installation
 Seminary, MS Optical Installation
 Jackson, LA Optical Installation

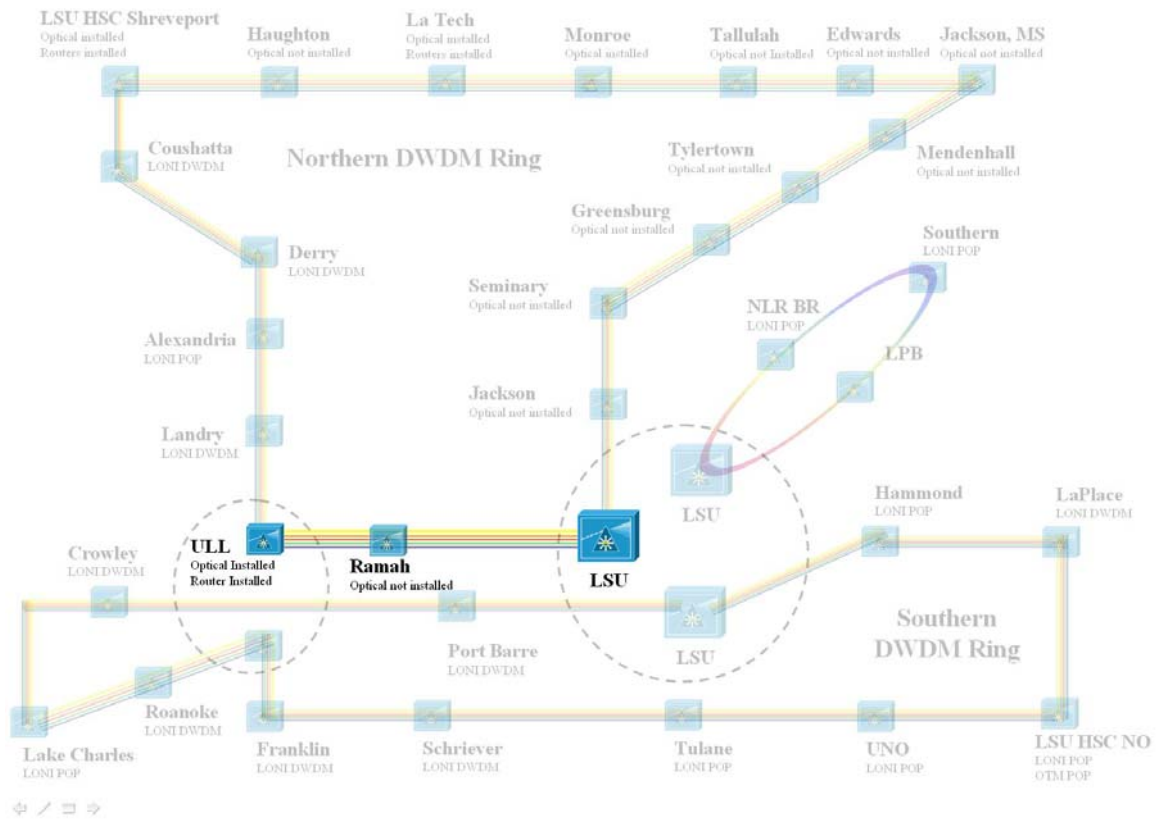

8/09/2006


Baton Rouge to Lafayette:

Completed

- LSU Optical and Routers Installation
- ULL Optical and Routers Installation
- Cisco Equipment Ordered (DCUs only)
- ULL P5 delivered and network completed
- Ramah Optical Installation
- Fiber Characterization complete from Ramah to Baton Rouge
- Route Construction for DOTD/Qwest
- ULL P5 Installation

Pending

- CEA
- Qwest Access
- BellSouth Local Loop in Baton Rouge has no completion date
- Site Survey of the Route to
- Fiber Assignments
- Fiber Characterization
- Cisco Equipment Delivery (DCU only) scheduled to arrive by August 15th

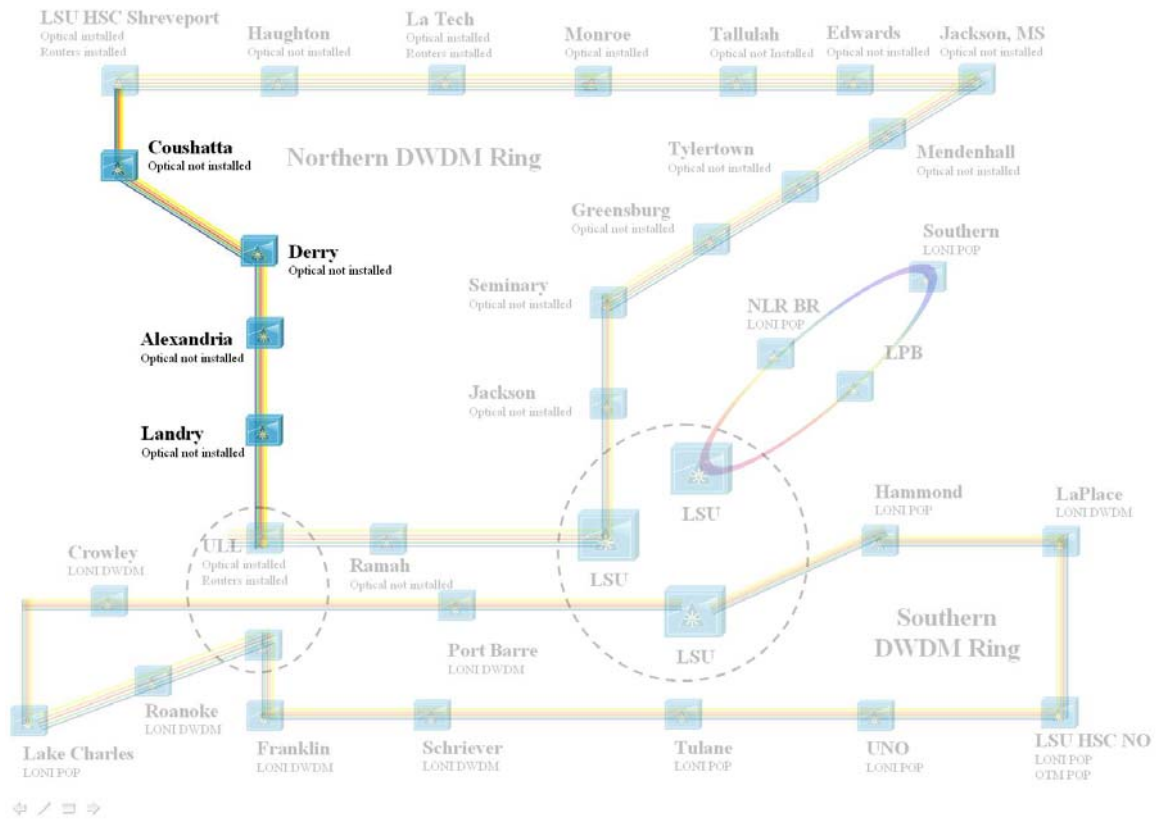

8/09/2006


Lafayette to Shreveport:

Completed

Award route to Sun America
Cisco Equipment Ordered (DCUs only)

Pending

CEA
IRU with Sun America
Site Survey of the Route
Fiber Assignments
Fiber Characterization
Cisco Equipment Delivery (DCU only) scheduled to arrive by August 15th
Landry Optical Installation
Alexandria Optical Installation
Derry Optical Installation
Coushatta Optical Installation

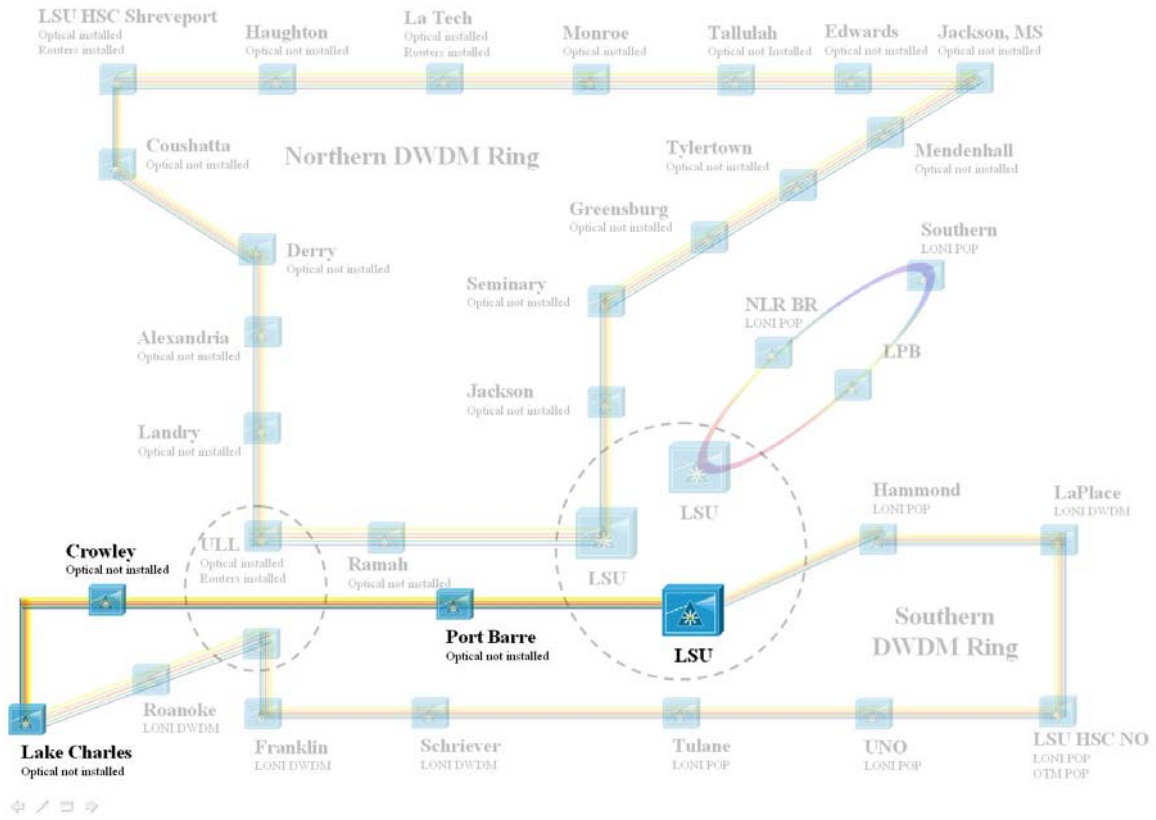

8/09/2006

Lake Charles to Baton Rouge:

Completed

Utilize AT&T Fiber

LSU Optical and Routers Installation

Pending

CEA

Route Construction by AT&T

Site Survey of the Route

Fiber Assignments

Fiber Characterization

BellSouth Local Loop in Lake Charles planned to be finished by August 25th


Lake Charles Optical and Routers Installation

Crowley Optical Installation

Port Barre Optical Installation

No responses to the Dark Fiber Bid opens June 20th

Cisco Equipment Order for LPB

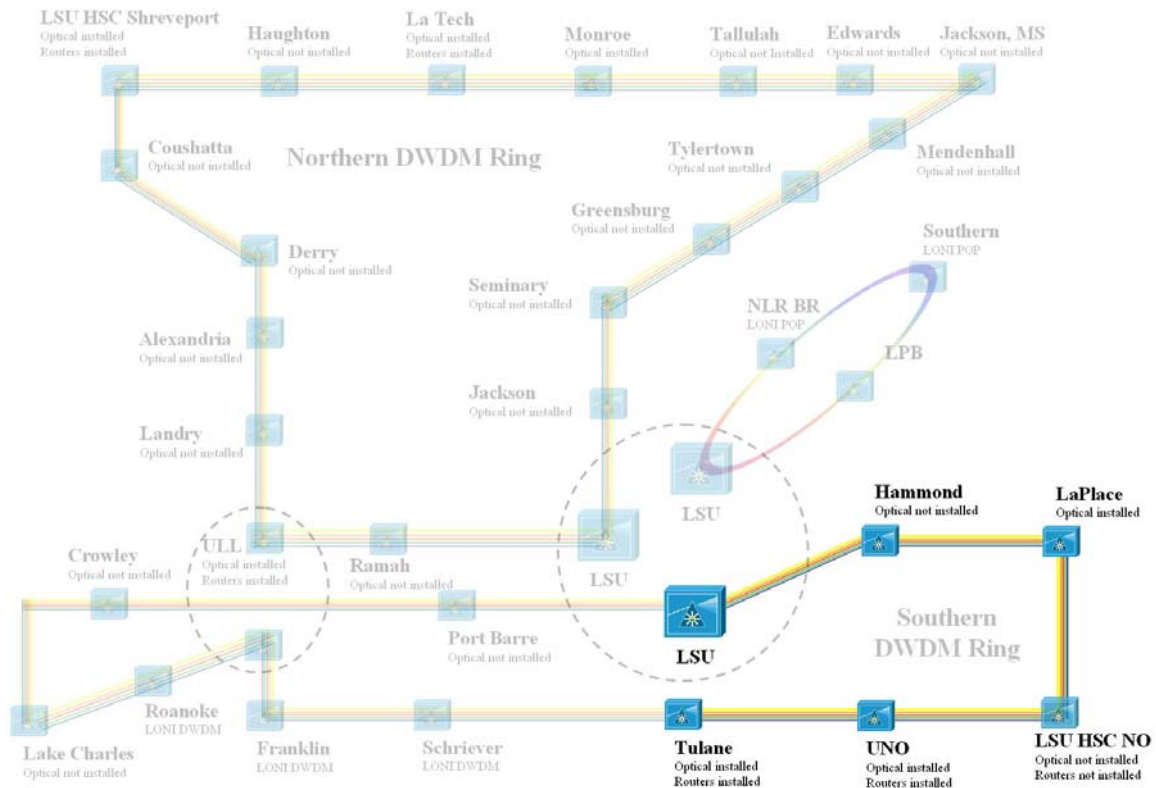

8/09/2006

Baton Rouge to New Orleans:


Completed

- LSU Optical and Routers Installation
- LaPlace Optical Installation
- Hammond to LaPlace Fiber is Lit
- UNO Optical and Routers Installation
- Tulane Routers Installation
- Tulane P5 Installation
- Cisco Equipment Order (DCUs only)
- Route Construction for DOTD/Qwest

Pending

- CEA
- Site Survey of the Route
- Fiber Assignments
- Fiber Characterization
- Cisco Equipment Order (DCUs only) scheduled to arrive by August 15th
- BellSouth Local Loop in Baton Rouge has no completion date
- BellSouth Local Loop in Hammond planned to be finished by August 21st
- BellSouth Local Loop in New Orleans planned to be finished by August 31st

HSC NO Optical and Routers Installation
No responses to the Dark Fiber Bid opens June 20th
UNO P5 Installation on August 28th

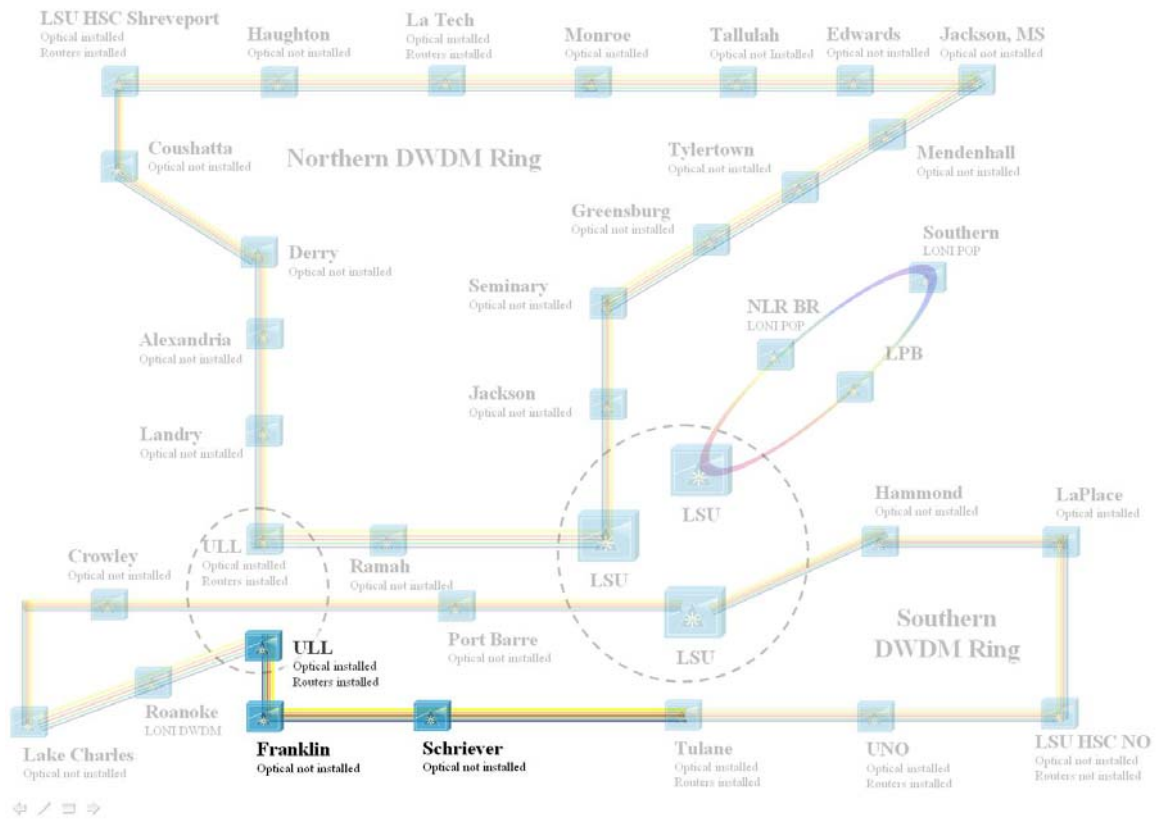

8/09/2006


New Orleans to Lafayette:

Completed

Award of Route to BellSouth
Cisco Equipment Order

Pending

IRU with BellSouth
Site Survey of the Route
Fiber Assignments
Fiber Characterization
Cisco Equipment Order scheduled to arrive by August 15th
BellSouth Loop Local in Lafayette planned to be finished by August 21st
Schriever Optical Installation
Franklin Optical Installation
No responses to the Dark Fiber Bid opens June 20th

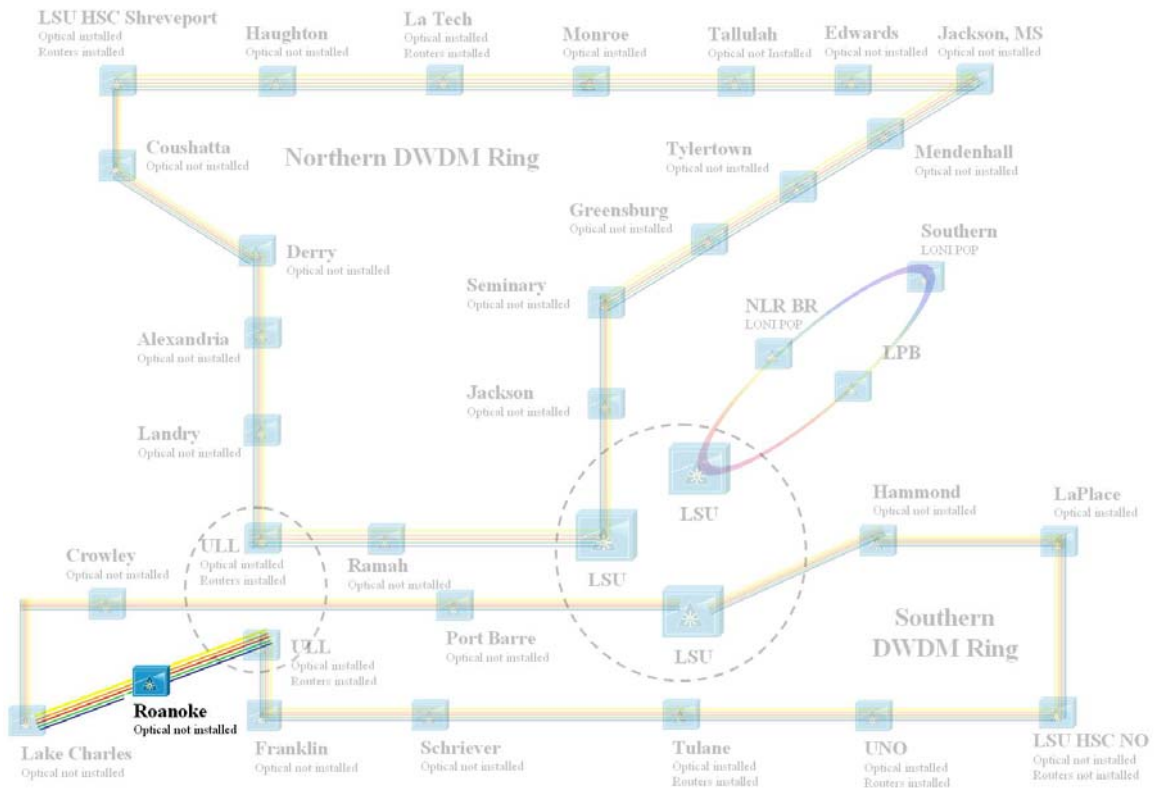

8/09/2006

Lafayette to Lake Charles:

Completed

Route Construction for DOTD/Qwest

Pending

CEA

Qwest Access

Site Survey of the Route

Fiber Assignments

Fiber Characterization


Cisco Equipment Order

Cisco Equipment Order for LPB

Roanoke Optical Installation

BellSouth Local Loop in Lake Charles planned to be finished by August 25th

No responses to the Dark Fiber Bid opens June 20th

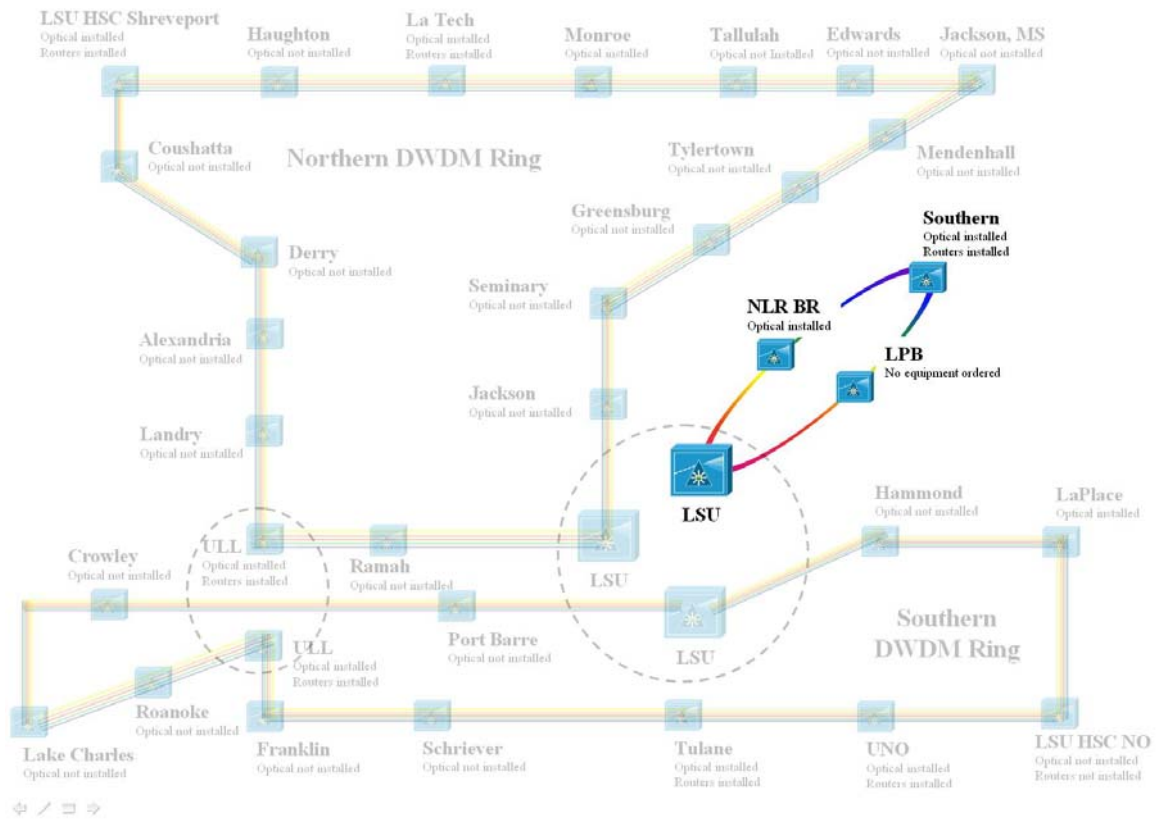

7/11/2006

Baton Rouge Ring:

Completed

- LSU Optical and Routers Installation
- NLR Optical Installation
- SU Optical and Routers Installation
- Cisco Equipment Order (DCUs only)
- (2) 10GE Circuits from LSU to SU
- (1) 10GE Circuit to NLR
- (1) 1GE Circuit to NLR

Pending

- Fiber Assignments
- Fiber Characterization
- Cisco Equipment Order (DCU only) scheduled to arrive by August 15th
- BellSouth Loop Local in Baton Rouge has no completion date
- No responses to the Dark Fiber Bids opens June 20th
- SU UPS Installation
- SU P5 Installation
- Cisco Equipment Order for LPB
