


☰ / ☰ ☰ ☰

7/11/2006

Overall:

- All remaining Cisco equipment should arrive by July 15th
- BellSouth is still working delivering local loops
- SU working on purchasing and installing UPS for P5
- UNO is on schedule to complete their electrical work for P5 by July 31<sup>st</sup>
- Route construction completed along I-10, I-12 and I-20
- ULL P5 delivered and network configured
- Targeting LONI peerings with LSU, SU and ULL by Fall Semester

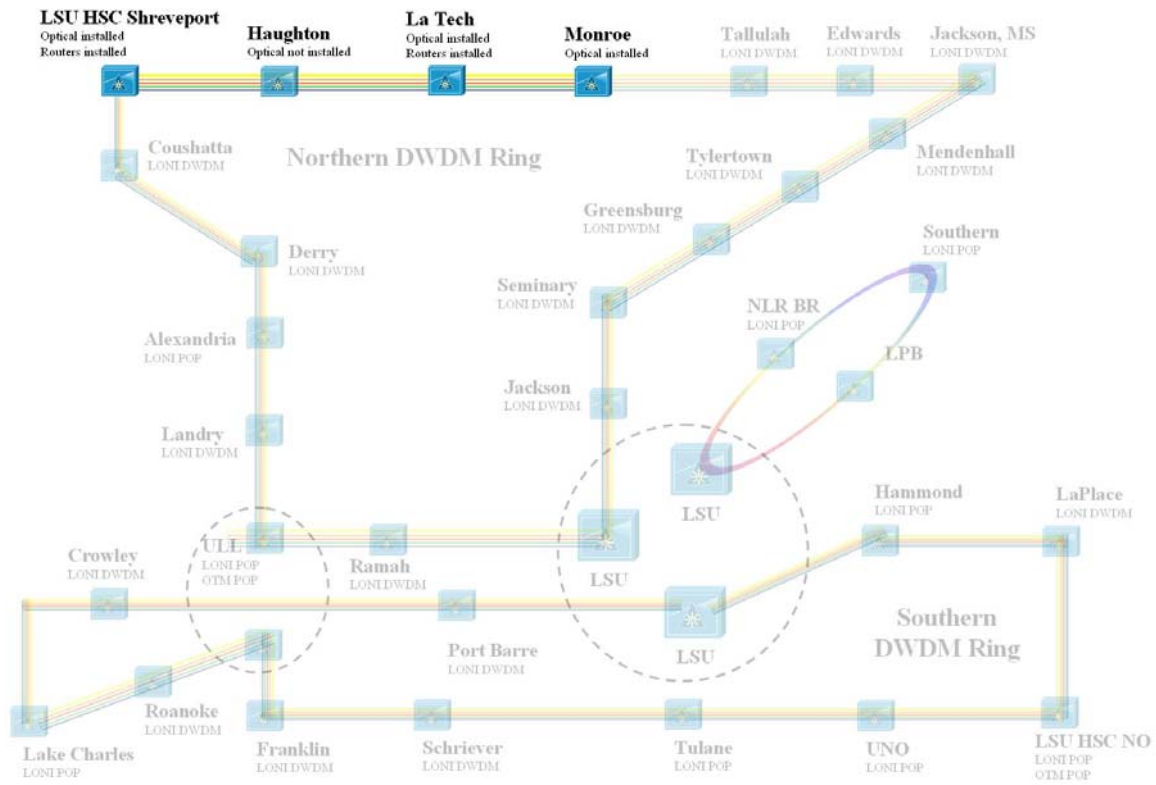

7/11/2006

Shreveport to Monroe:

Completed

HSC Shreveport Optical and Routers Installation

La Tech Optical and Routers Installation

Monroe Optical Installation

La Tech P5 Installation

Cisco Equipment Ordered (DCUs only)


❖ Route Construction for McLeodUSA

Pending

CEA

Fiber Characterization

- ❖ BellSouth Local Loop in Shreveport has no completion date
- ❖ BellSouth Local Loop in Ruston planned to be finished by August 11th
- ❖ BellSouth Local Loop in Monroe has no completion date
- ❖ Cisco Equipment Delivery (DCUs only) scheduled to arrive by July 15th
- ❖ Haughton Optical Installation
- ❖ No responses to the Dark Fiber Bid opens June 20th

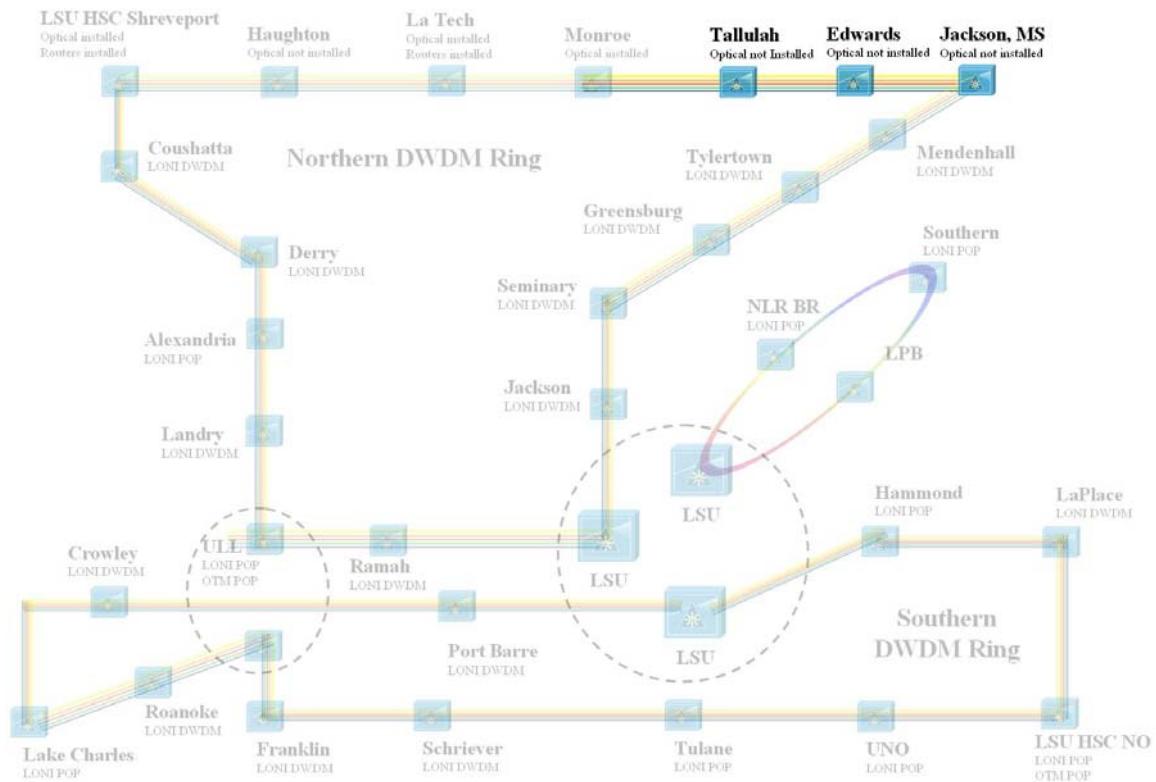

7/11/2006


Monroe to Jackson, MS:

Completed

Award of route to ITC^DeltaCom  
 Site Survey of the Route  
 Cisco Equipment Ordered

Pending

- Fiber Assignments
- Fiber Characterization
- ❖ BellSouth Local Loop in Monroe has no completion date
- ❖ Cisco Equipment Delivery scheduled to arrive by July 15th
- Tallulah Optical Installation
- Edwards Optical Installation
- Jackson, MS Optical Installation
- There were no responses to City of Jackson, MS Local Loop Bid opens June 6th

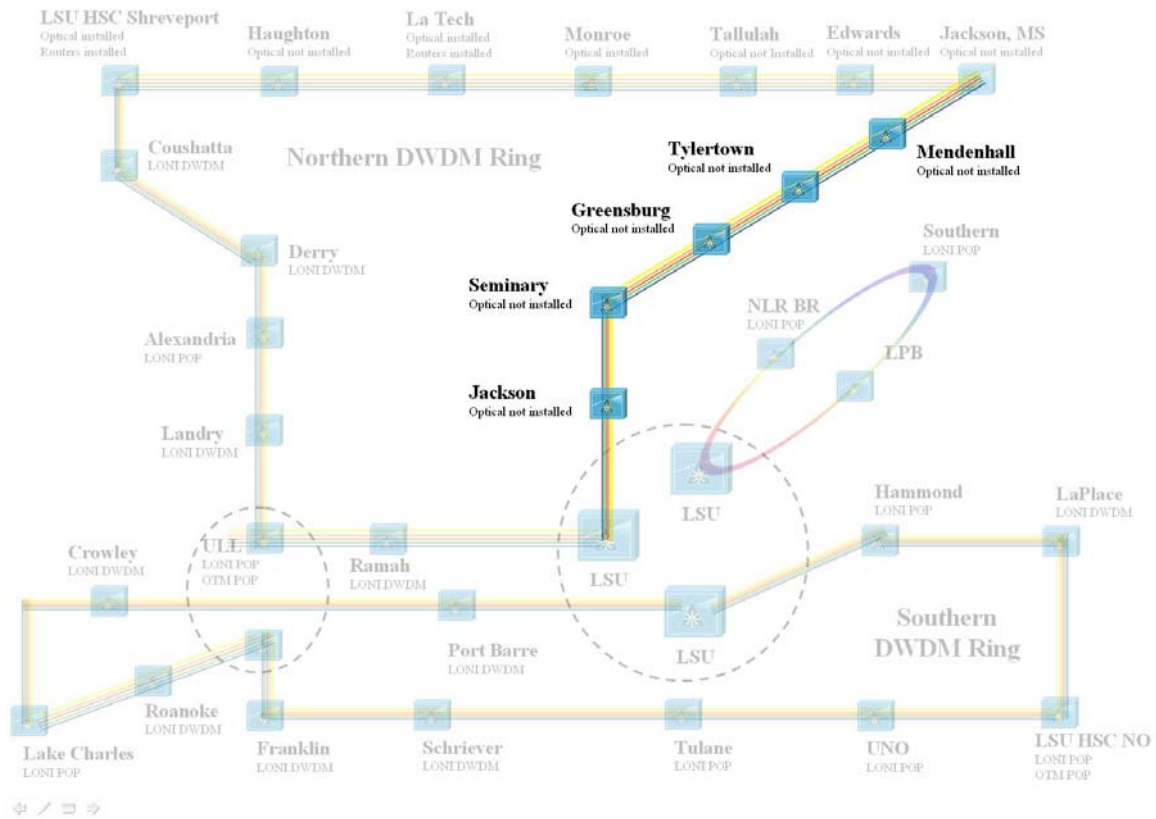

7/11/2006

Jackson, MS to Baton Rouge:


Completed

Award of Route to WilTel/Level3  
 Cisco Equipment Ordered  
 WilTel/Level3 Kick-off

Pending

Site Survey of the Route  
 Fiber Assignments  
 Fiber Characterization

- ❖ Cisco Equipment Delivery scheduled to arrive by July 15th
- Mendenhall, MS Optical Installation
- Tylertown, MS Optical Installation
- Greensburg, MS Optical Installation
- Seminary, MS Optical Installation
- Jackson, LA Optical Installation

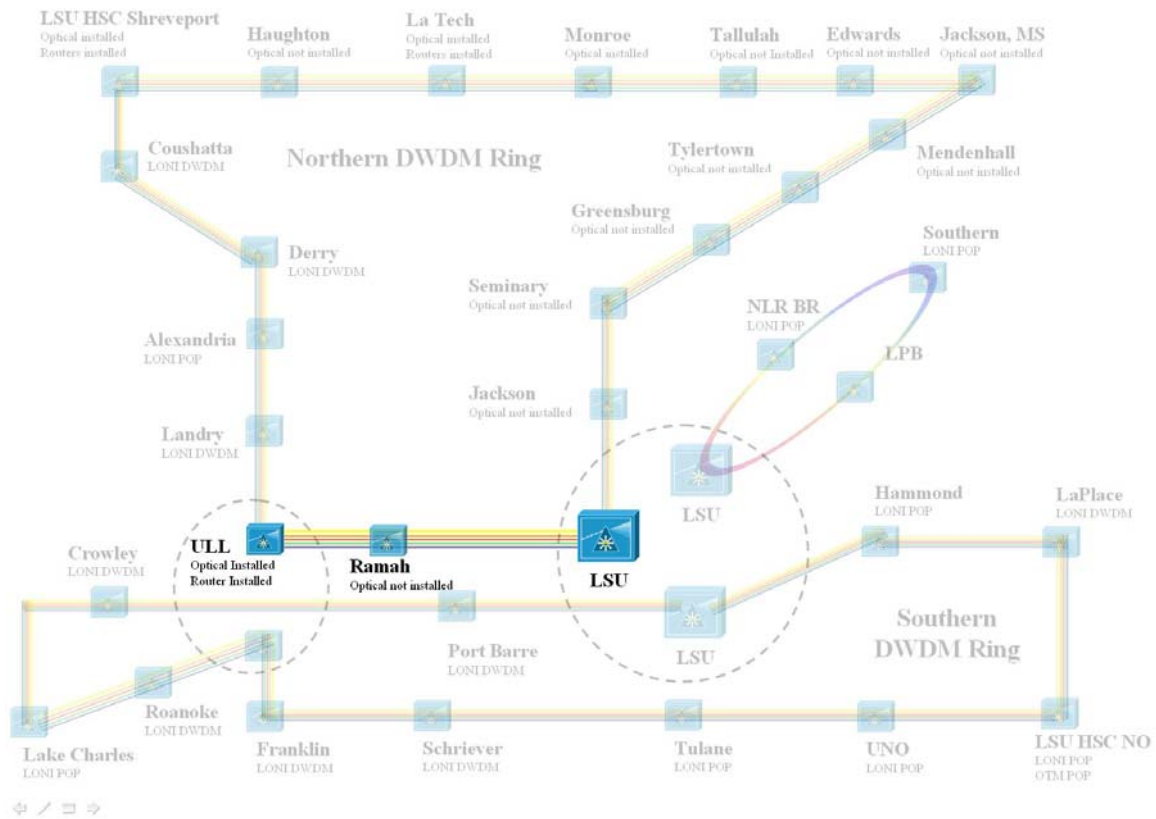

7/11/2006

Baton Rouge to Lafayette:


Completed

- LSU Optical and Routers Installation
- ULL Optical and Routers Installation
- Cisco Equipment Ordered (DCUs only)

- ❖ ULL P5 delivered and network completed
- ❖ Ramah Optical Installation
- ❖ Fiber Characterization complete from Ramah to Baton Rouge
- ❖ Route Construction for DOTD/Qwest

Pending

- CEA
- Qwest Access
- ❖ BellSouth Local Loop in Baton Rouge has no completion date
- Site Survey of the Route to
- Fiber Assignments
- Fiber Characterization
- ❖ Cisco Equipment Delivery (DCU only) scheduled to arrive by July 15th
- ❖ ULL P5 Installation scheduled for week for July 10th

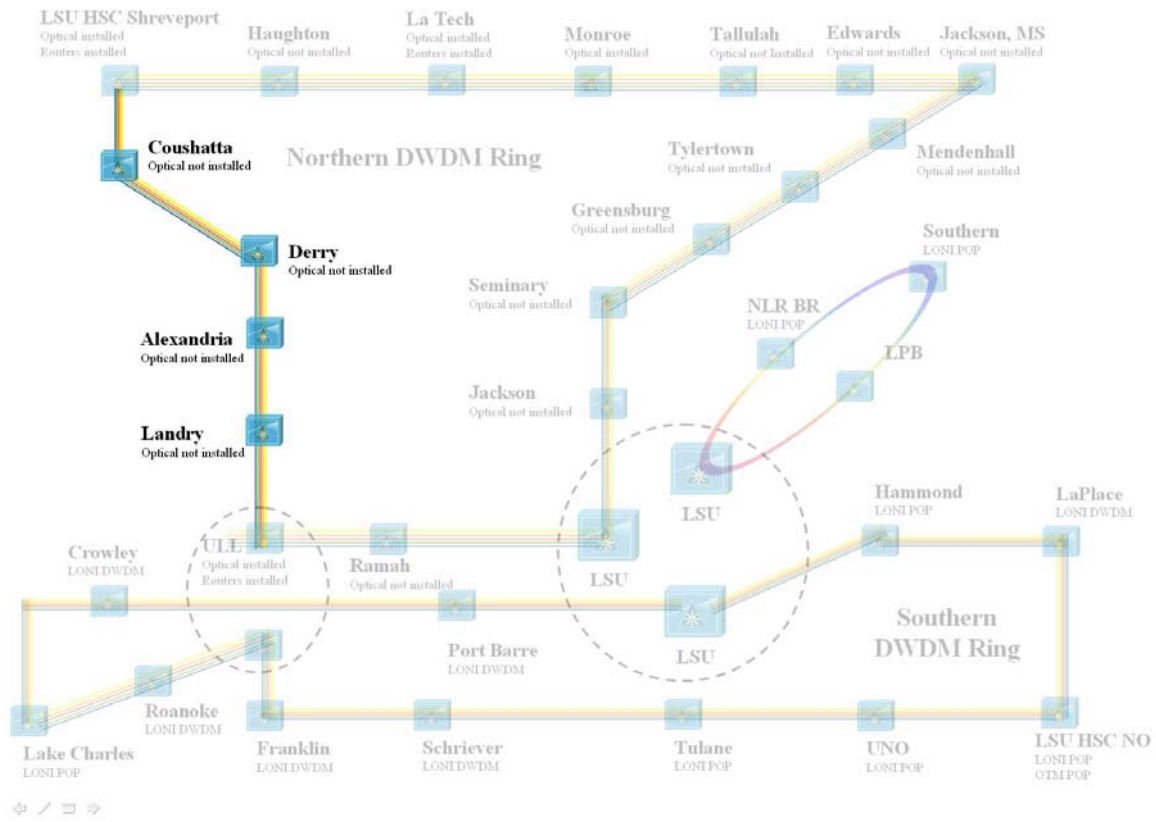

7/11/2006


Lafayette to Shreveport:

Completed

Award route to Sun America  
Cisco Equipment Ordered (DCUs only)

Pending

CEA  
IRU with Sun America  
Site Survey of the Route  
Fiber Assignments  
Fiber Characterization  
❖ Cisco Equipment Delivery (DCU only) scheduled to arrive by July 15th  
Landry Optical Installation  
Alexandria Optical Installation  
Derry Optical Installation  
Coushatta Optical Installation

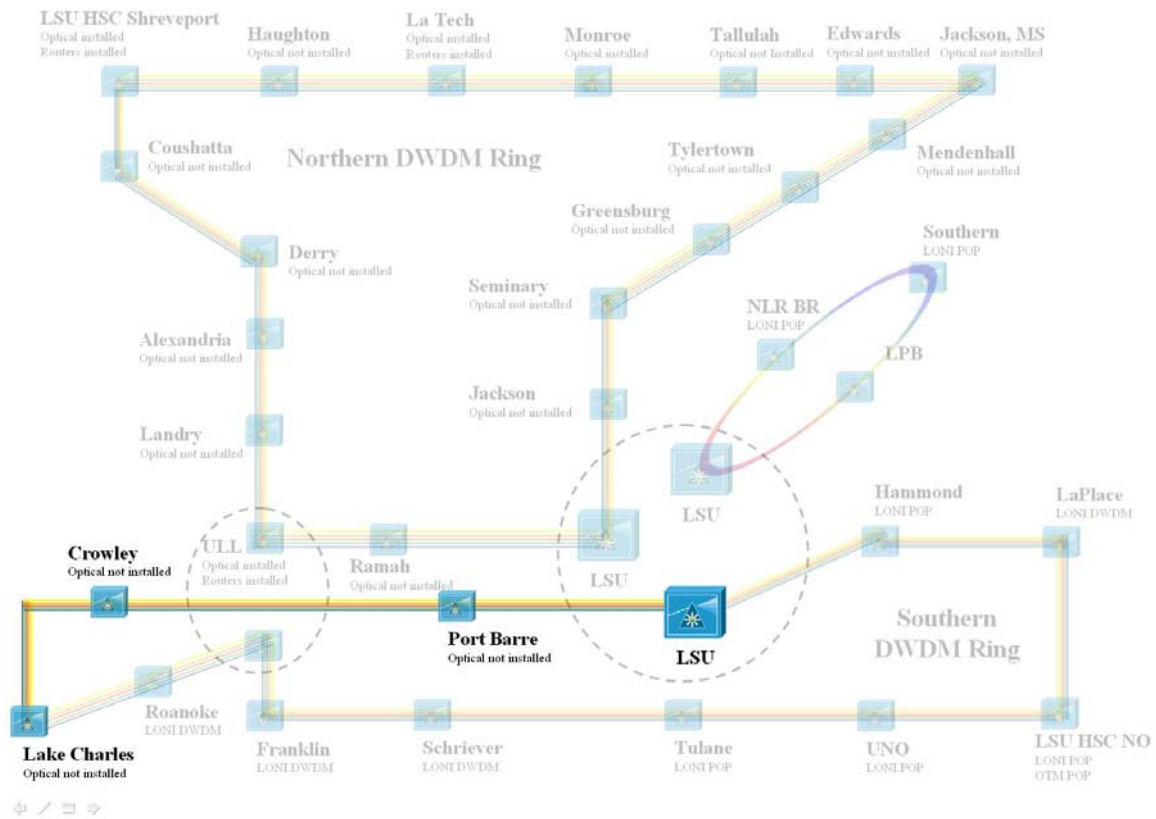

7/11/2006

Lake Charles to Baton Rouge:

Completed

Utilize AT&T Fiber

LSU Optical and Routers Installation

Pending

CEA

Route Construction by AT&T

Site Survey of the Route

Fiber Assignments

Fiber Characterization


❖ BellSouth Local Loop in Lake Charles planned to be finished by August 25th

Lake Charles Optical and Routers Installation

Crowley Optical Installation

Port Barre Optical Installation

❖ No responses to the Dark Fiber Bid opens June 20<sup>th</sup>  
Cisco Equipment Order for LPB

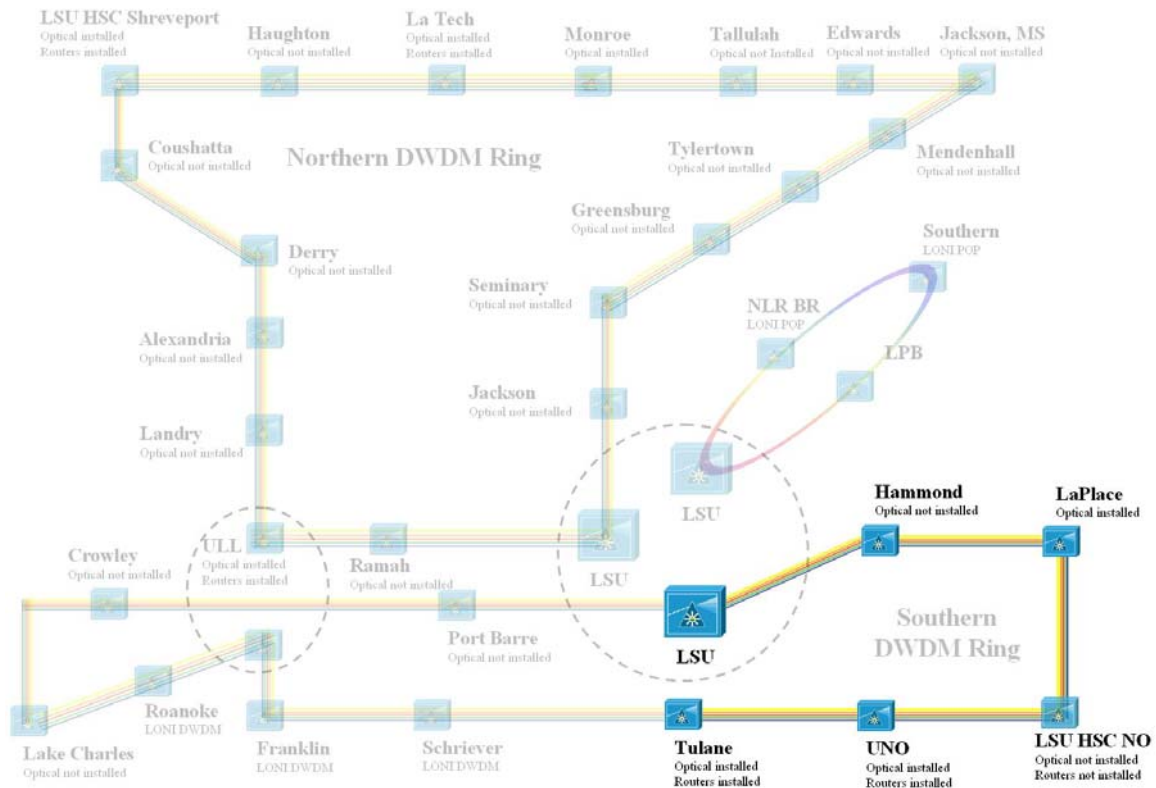

7/11/2006

Baton Rouge to New Orleans:

Completed

- LSU Optical and Routers Installation
- LaPlace Optical Installation
- Hammond to LaPlace Fiber is Lit
- UNO Optical and Routers Installation
- Tulane Routers Installation
- Tulane P5 Installation
- Cisco Equipment Order (DCUs only)


❖ Route Construction for DOTD/Qwest

Pending

- CEA
- Site Survey of the Route
- Fiber Assignments
- Fiber Characterization
- ❖ Cisco Equipment Order (DCUs only) scheduled to arrive by July 15th
- ❖ BellSouth Local Loop in Baton Rouge has no completion date
- ❖ BellSouth Local Loop in Hammond planned to be finished by August 21st
- ❖ BellSouth Local Loop in New Orleans planned to be finished by July 31st
- HSC NO Optical and Routers Installation



- ❖ No responses to the Dark Fiber Bid opens June 20th  
UNO P5 Installation

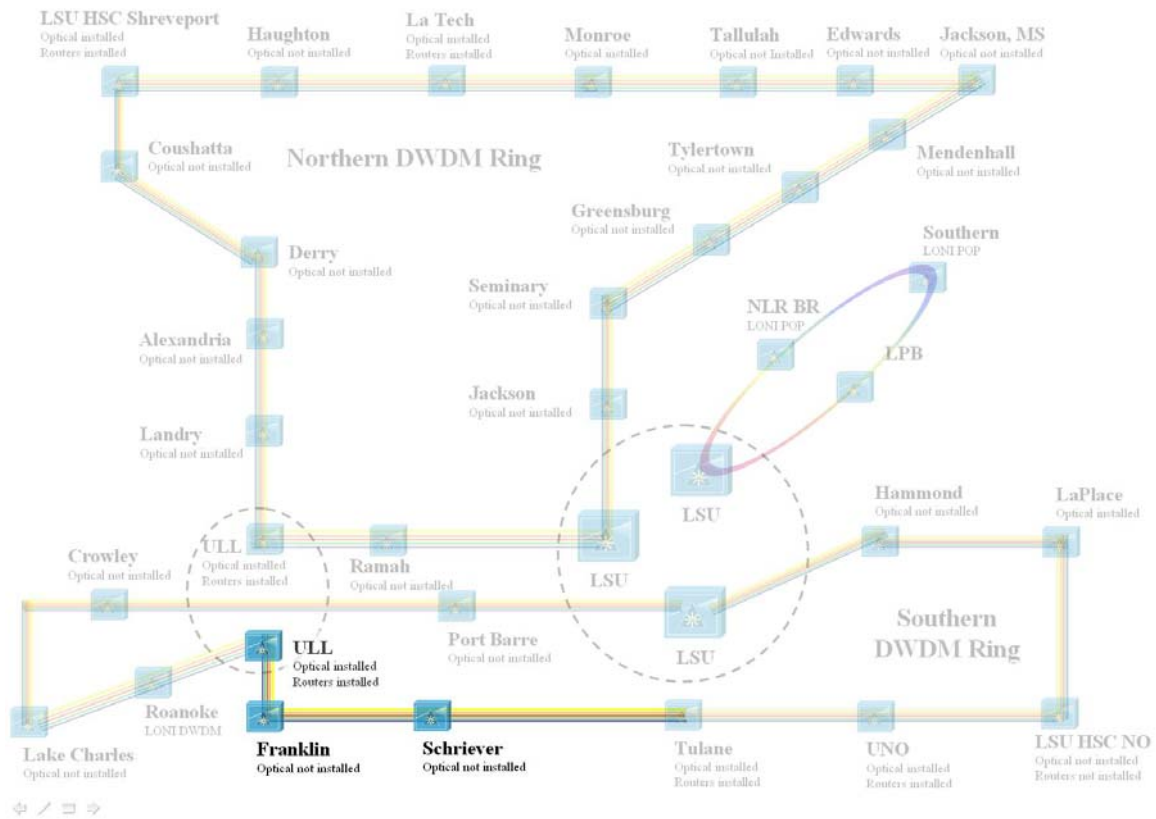

7/11/2006

New Orleans to Lafayette:


Completed

Award of Route to BellSouth  
Cisco Equipment Order

Pending

IRU with BellSouth  
Site Survey of the Route  
Fiber Assignments  
Fiber Characterization

- ❖ Cisco Equipment Order scheduled to arrive by July 15th
- ❖ BellSouth Loop Local in Lafayette planned to be finished by August 21st
- ❖ Schriever Optical Installation
- ❖ Franklin Optical Installation
- ❖ No responses to the Dark Fiber Bid opens June 20th

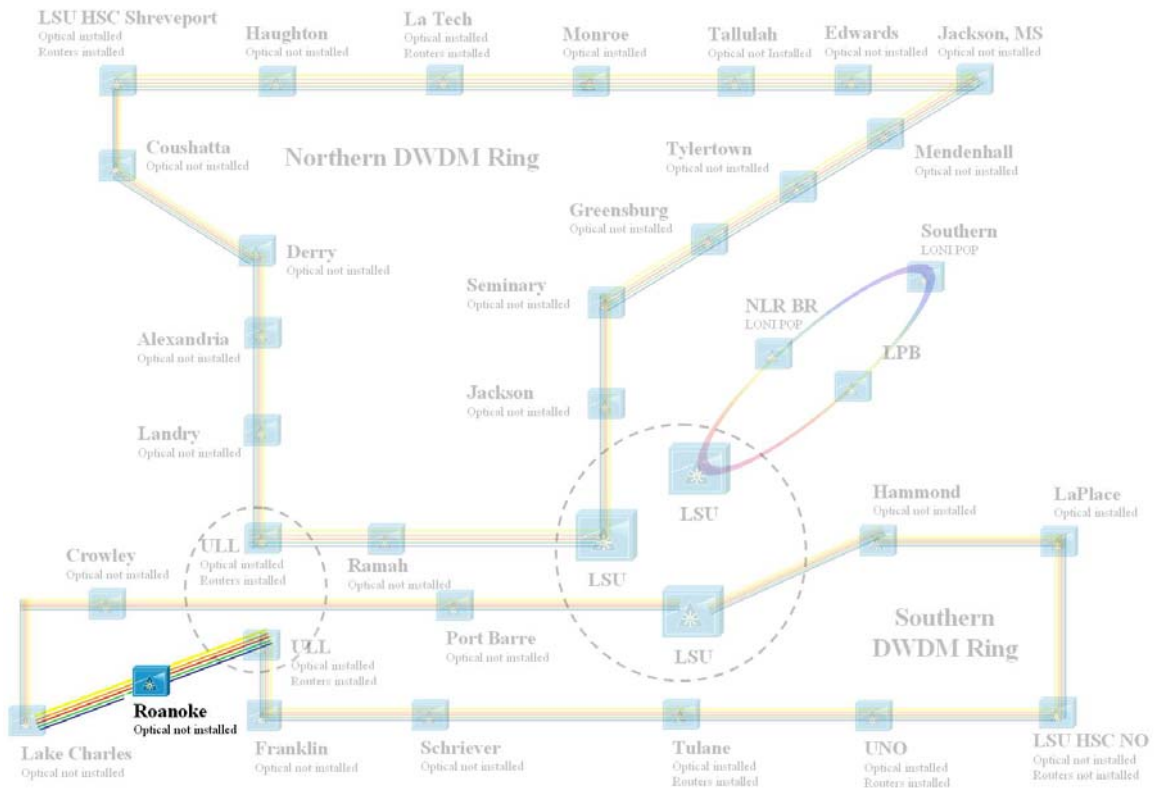

7/11/2006

Lafayette to Lake Charles:

Completed

❖ Route Construction for DOTD/Qwest

Pending

CEA

Qwest Access

Site Survey of the Route

Fiber Assignments

Fiber Characterization


Cisco Equipment Order

Cisco Equipment Order for LPB

Roanoke Optical Installation

❖ BellSouth Local Loop in Lake Charles planned to be finished by August 25th

❖ No responses to the Dark Fiber Bid opens June 20th

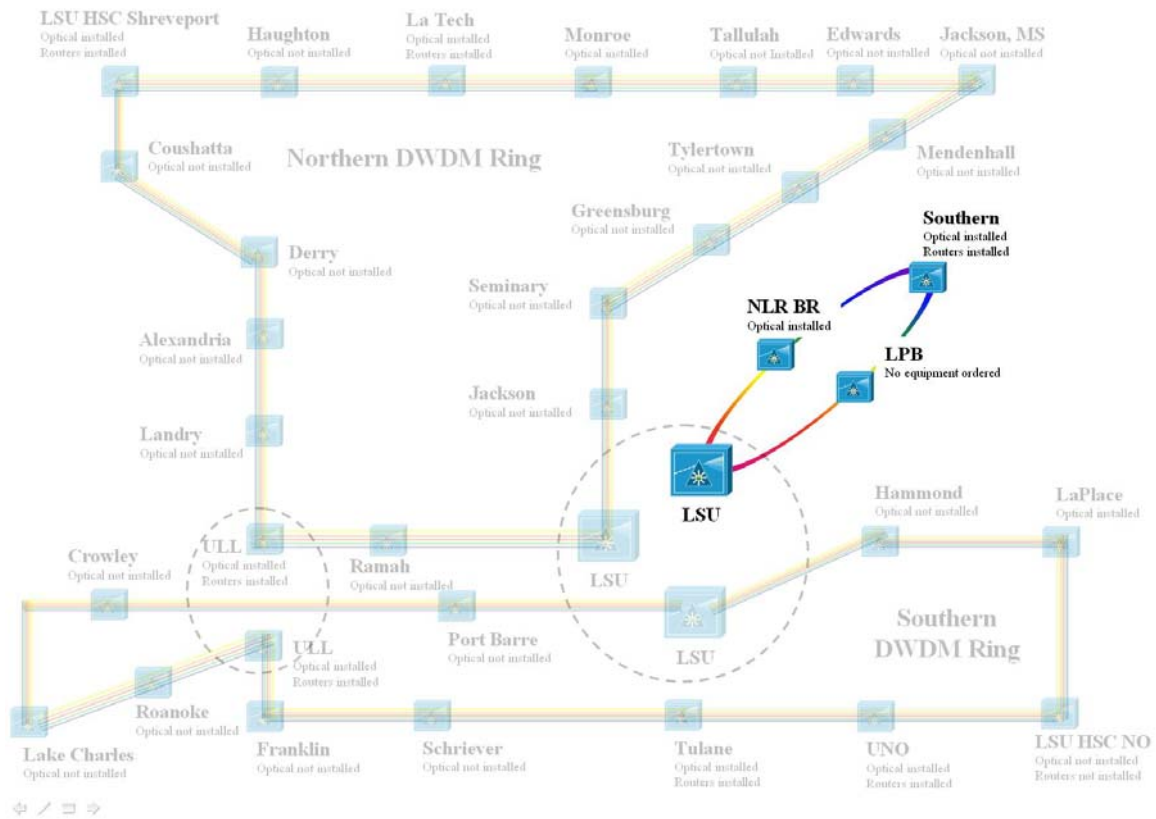

7/11/2006

Baton Rouge Ring:

Completed

- LSU Optical and Routers Installation
- NLR Optical Installation
- SU Optical and Routers Installation
- Cisco Equipment Order (DCUs only)
- (2) 10GE Circuits from LSU to SU
- (1) 10GE Circuit to NLR
- (1) 1GE Circuit to NLR

Pending

- Fiber Assignments
- Fiber Characterization
- ❖ Cisco Equipment Order (DCU only) scheduled to arrive by July 15th
- ❖ BellSouth Loop Local in Baton Rouge has no completion date
- ❖ No responses to the Dark Fiber Bids opens June 20<sup>th</sup>
- ❖ SU UPS Installation
- SU P5 Installation
- Cisco Equipment Order for LPB
