

6/13/2006

Shreveport to Monroe:

Completed

HSC Shreveport Optical and Routers Installation

La Tech Optical and Routers Installation

Monroe Optical Installation


La Tech P5 Installation

Cisco Equipment Ordered (DCUs only)

Pending

CEA

- ❖ Route Construction by McLeodUSA planned to be finished by June 30th
- Fiber Characterization
- ❖ BellSouth Local Loop in Shreveport has no completion date
- ❖ BellSouth Local Loop in Ruston planned to be finished by June 30th
- ❖ BellSouth Local Loop in Monroe planned to be finished by June 30th
- ❖ Cisco Equipment Delivery (DCUs only) scheduled to arrive by July 31st
- Haughton Optical Installation
- Dark Fiber Bid opens June 20th

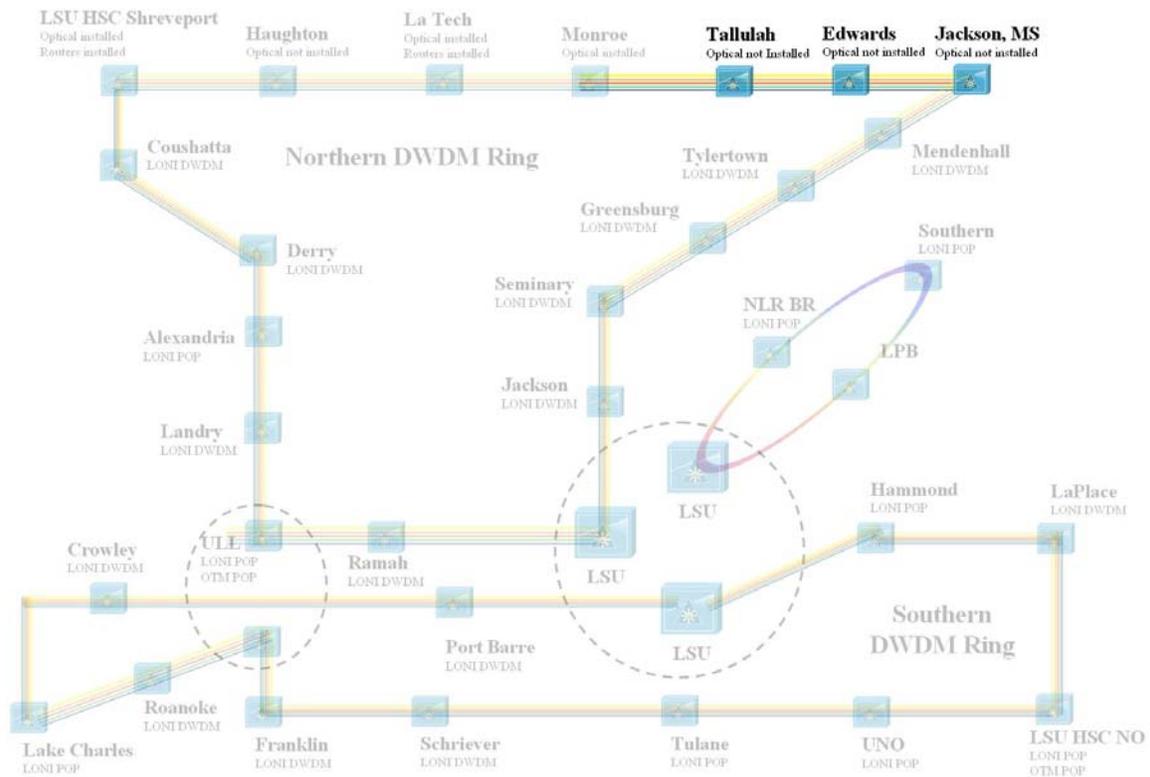

6/13/2006


Monroe to Jackson, MS:

Completed

Award of route to ITC^DeltaCom
 Site Survey of the Route
 Cisco Equipment Ordered

Pending

- Fiber Assignments
- Fiber Characterization
- ❖ BellSouth Local Loop in Monroe planned to be finished by June 30th
- ❖ Cisco Equipment Delivery scheduled to arrive by August 10th
- Tallulah Optical Installation
- Edwards Optical Installation
- Jackson, MS Optical Installation
- ❖ There were no responses to City of Jackson, MS Local Loop Bid opens June 6th

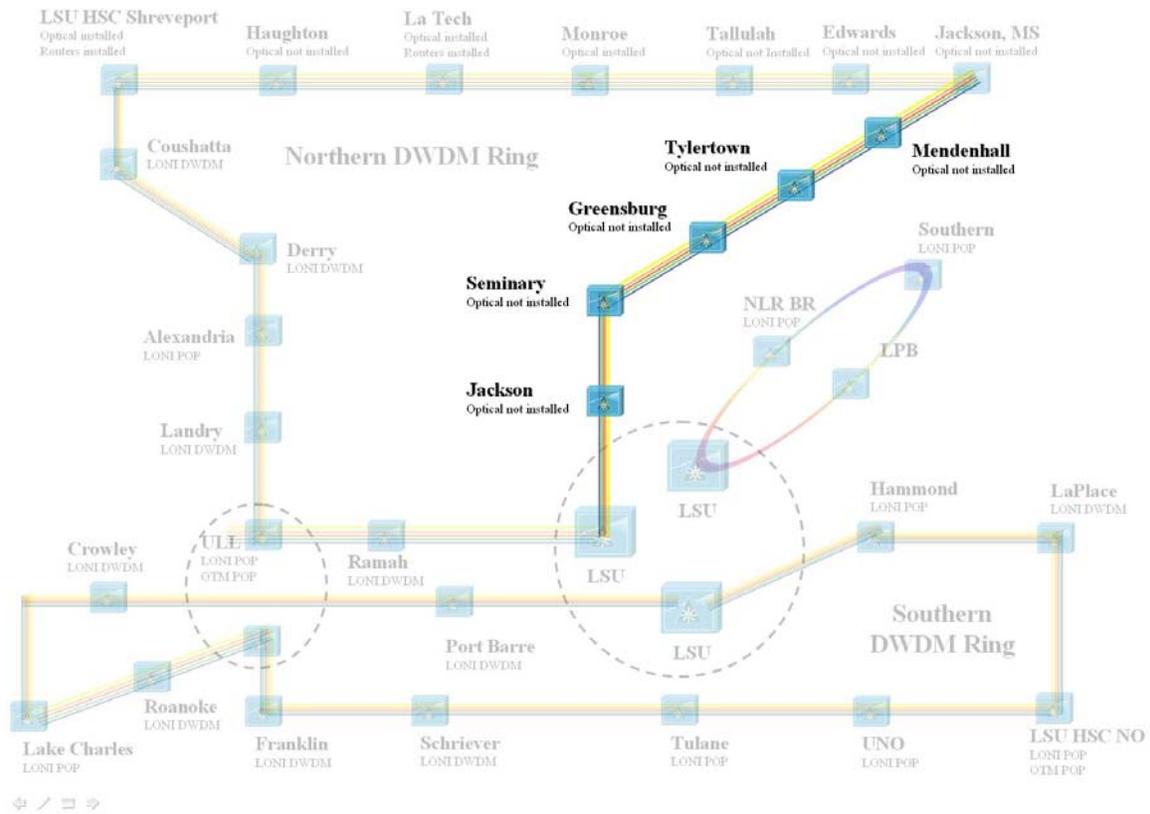

6/13/2006

Jackson, MS to Baton Rouge:

Completed

Award of Route to WilTel/Level3

Cisco Equipment Ordered

❖ WilTel/Level3 Kick-off

Pending

Site Survey of the Route

Fiber Assignments

Fiber Characterization

❖ Cisco Equipment Delivery scheduled to arrive by July 15th


Mendenhall, MS Optical Installation

Tylertown, MS Optical Installation

Greensburg, MS Optical Installation

Seminary, MS Optical Installation

Jackson, LA Optical Installation

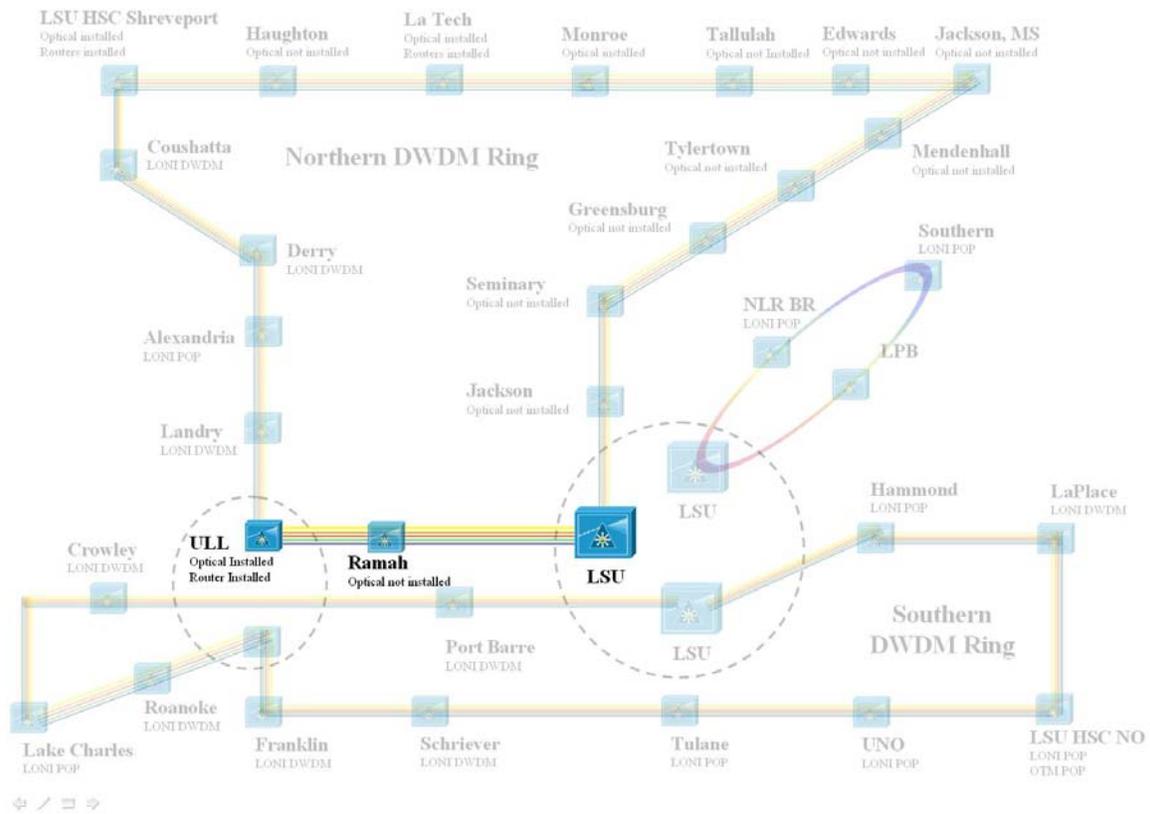

6/13/2006


Baton Rouge to Lafayette:

Completed

- LSU Optical and Routers Installation
- ULL Optical and Routers Installation
- Cisco Equipment Ordered (DCUs only)

Pending

- CEA
- Qwest Access
- ❖ BellSouth Local Loop in Baton Rouge has no completion date
- Site Survey of the Route to
- Fiber Assignments
- Fiber Characterization
- ❖ Cisco Equipment Delivery (DCU only) scheduled to arrive by August 10th
- Ramah Optical Installation
- ULL P5 Installation scheduled for June 26th

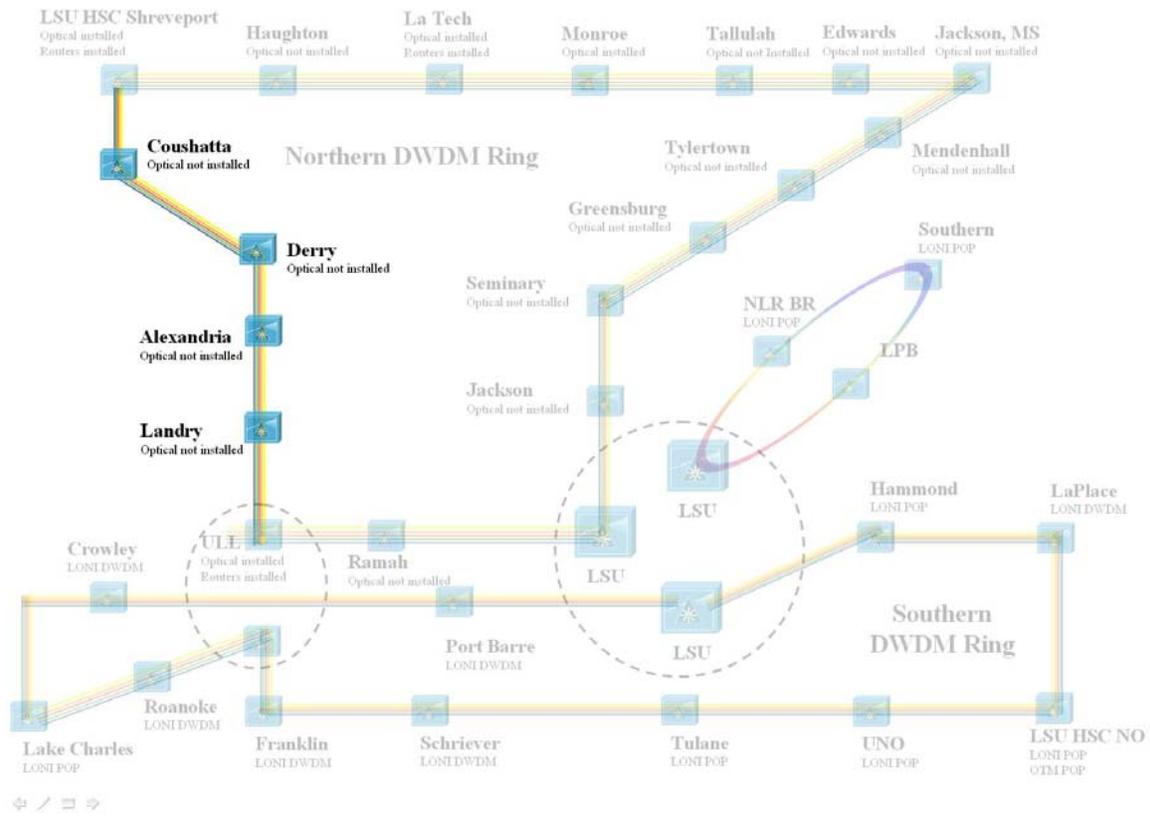

6/13/2006


Lafayette to Shreveport:

Completed

Award route to Sun America
Cisco Equipment Ordered (DCUs only)

Pending

CEA
IRU with Sun America
Site Survey of the Route
Fiber Assignments
Fiber Characterization
❖ Cisco Equipment Delivery (DCU only) scheduled to arrive by August 10th
Landry Optical Installation
Alexandria Optical Installation
Derry Optical Installation
Coushatta Optical Installation

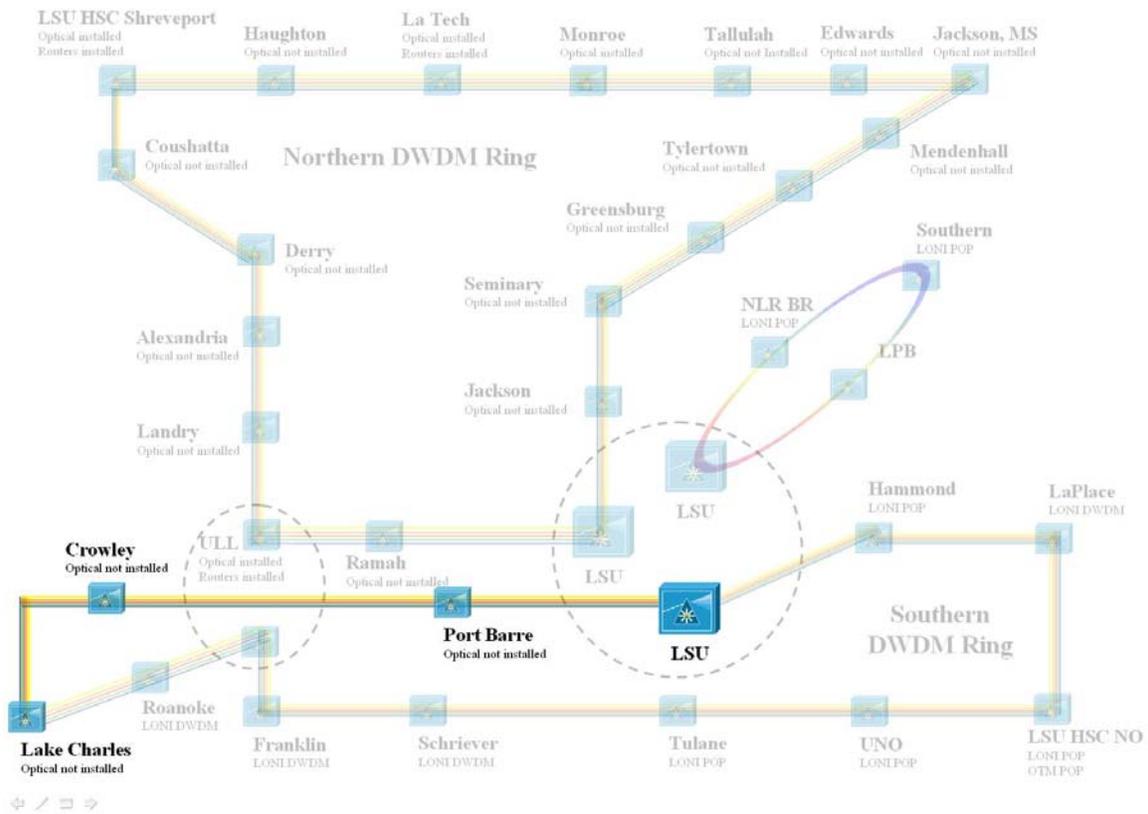

6/13/2006

Lake Charles to Baton Rouge:

Completed

Utilize AT&T Fiber

LSU Optical and Routers Installation

Pending

CEA

Route Construction by AT&T

Site Survey of the Route

Fiber Assignments

Fiber Characterization



BellSouth Local Loop in Lake Charles planned to be finished by July 31st


Cisco Equipment Order for LPB

Lake Charles Optical and Routers Installation

Crowley Optical Installation

Port Barre Optical Installation

Dark Fiber Bid opens June 20th

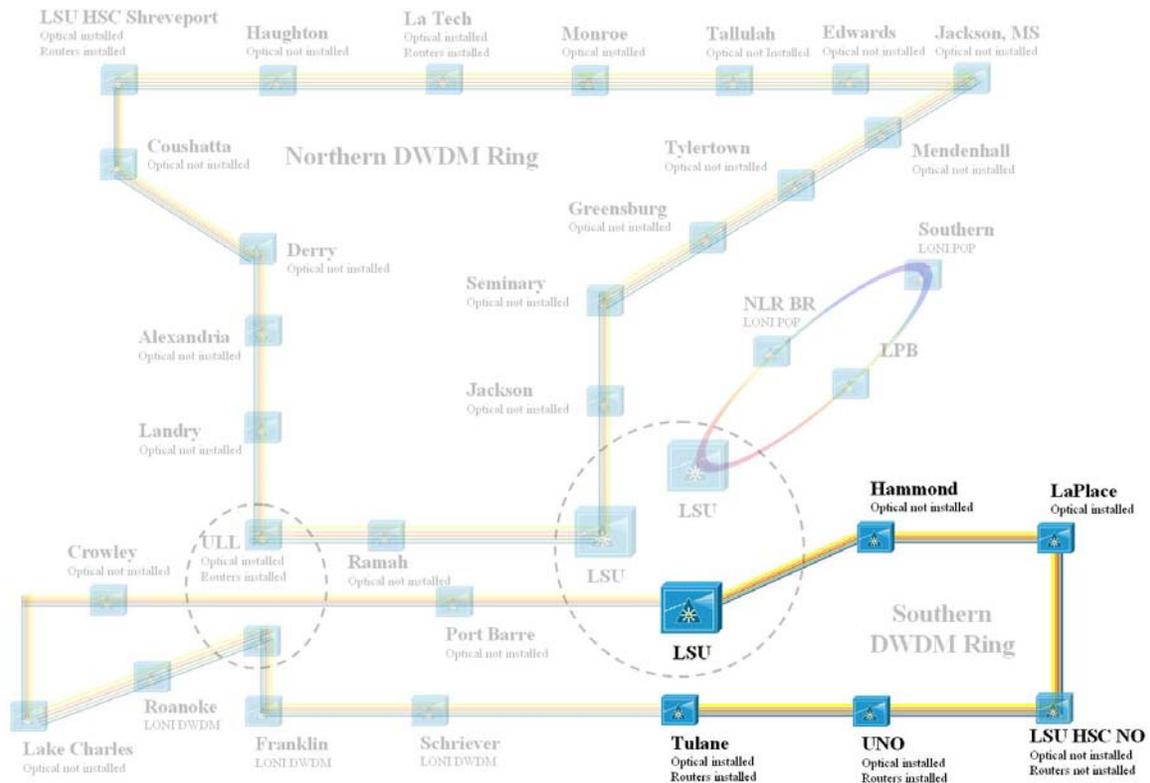

6/13/2006


Baton Rouge to New Orleans:

Completed

- LSU Optical and Routers Installation
- LaPlace Optical Installation
- Hammond to LaPlace Fiber is Lit
- UNO Optical and Routers Installation
- Tulane Routers Installation
- Tulane P5 Installation
- Cisco Equipment Order (DCUs only)

Pending

- CEA
- Site Survey of the Route
- Fiber Assignments
- Fiber Characterization
- ❖ Cisco Equipment Order (DCUs only) scheduled to arrive by June 30th
- ❖ BellSouth Local Loop in Baton Rouge has no completion date
- ❖ BellSouth Local Loop in Hammond planned to be finished by July 31st
- ❖ BellSouth Local Loop in New Orleans planned to be finished by July 31st
- HSC NO Optical and Routers Installation
- Dark Fiber Bid opens June 20th
- UNO P5 Installation

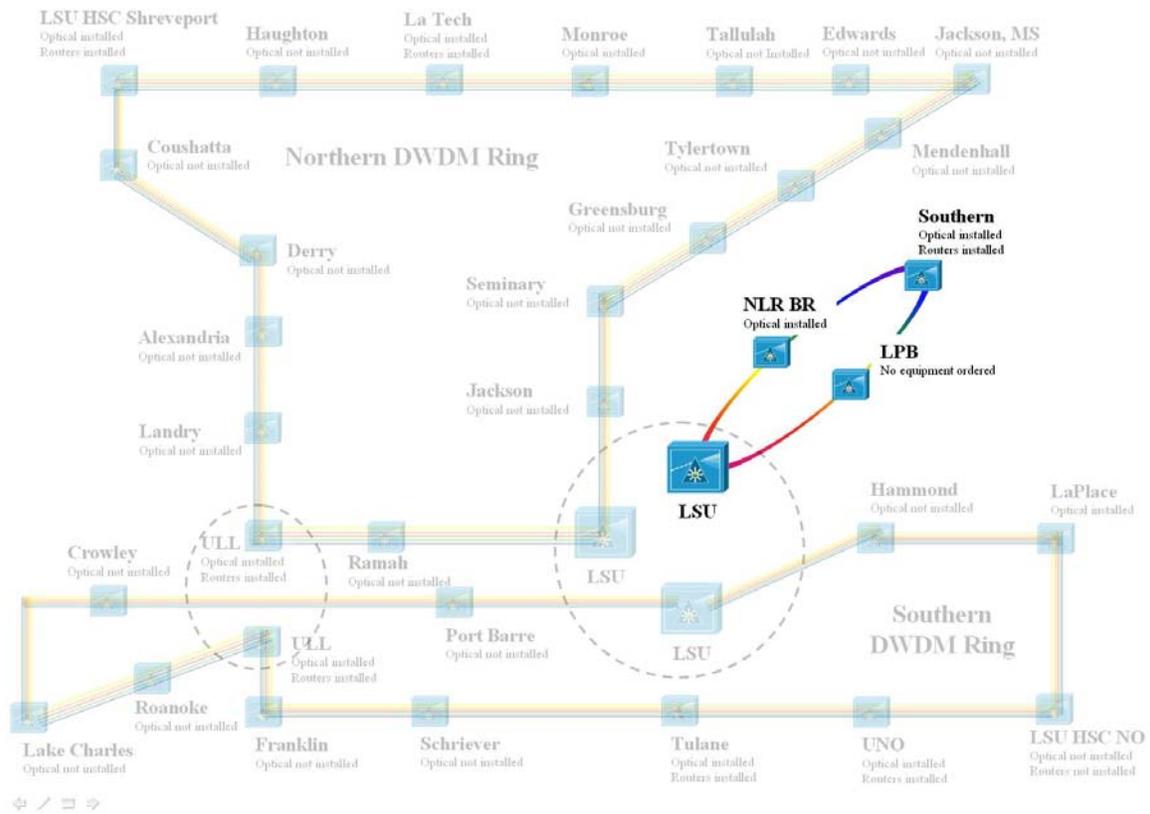

6/13/2006

Baton Rouge Ring:

Completed

- LSU Optical and Routers Installation
- NLR Optical Installation
- SU Optical and Routers Installation
- Cisco Equipment Order (DCUs only)
- (2) 10GE Circuits from LSU to SU
- (1) 10GE Circuit to NLR
- (1) 1GE Circuit to NLR

Pending

- Fiber Assignments
- Fiber Characterization
- ❖ Cisco Equipment Order (DCU only) scheduled to arrive by June 30th
- ❖ BellSouth Loop Local in Baton Rouge has no completion date
- Dark Fiber Bids opens June 20th
- SU P5 Installation
- Cisco Equipment Order for LPB
