


## Planned

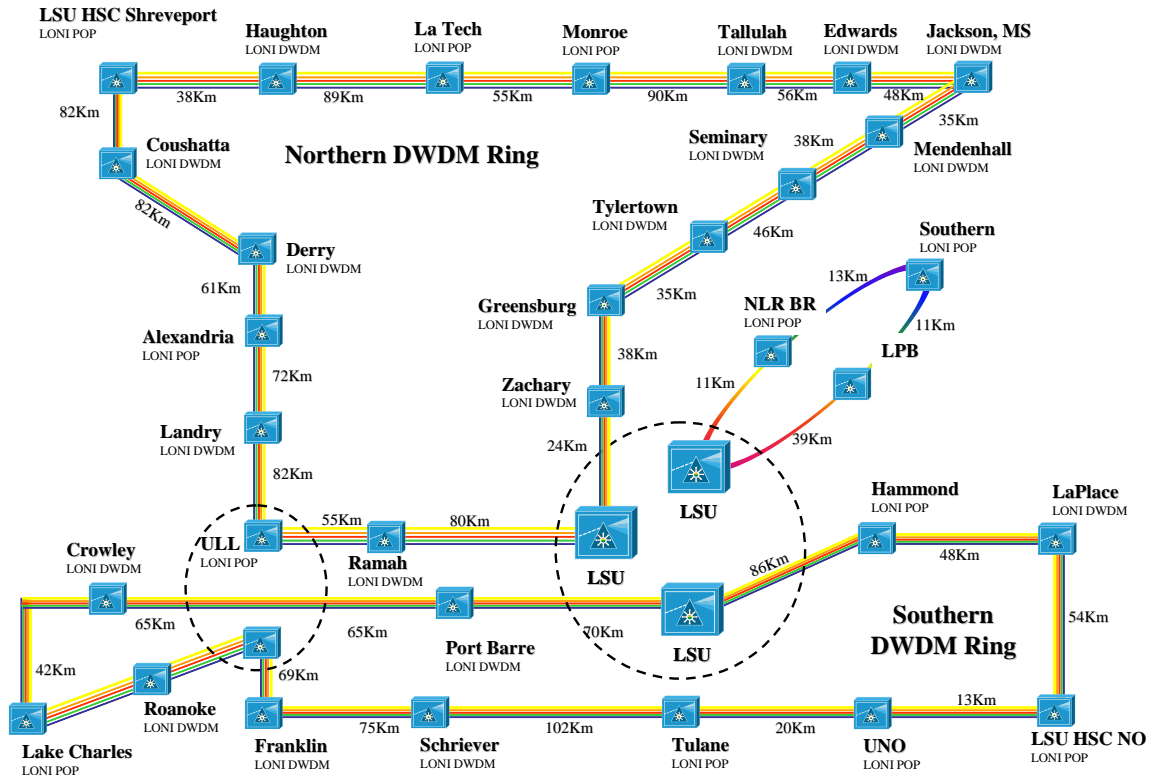

## Phase 2 Accomplishments

- Connected SELU, LPB, ISB, LSU-S, ULM, Delgado CC, BRCC, BPCC, LTC-Port Allen, LTC-Headquarters, LTC-Bastrop Airport
- Activated (1) 10GE circuits
- Installed (4) Cisco 6500s
- LONI router configuration for LCTCS complete in Baton Rouge, Monroe, Shreveport and Lafayette
- Moved Tulane Campus to LONI 10GE
- Fiber characterization between Lafayette and Lake Charles
- Metro-Ethernet to ISB supporting LSU AgCenter WAN

Short-term Plans:

- LCTCS in New Orleans, Alexandria and Lake Charles should be connected by end of July
- Install optical amplifier in Zachary
- LONI connection to LSU-E ordered
- LONI connection to SU-Shreveport delivered but not configured
- LONI connection to BoR at NTG delivered but waiting on NTG extension
- LONI connection to LSU HSC New Orleans to DPS delivered but not configured
- Deliver routers and optical equipment to NSU
- Waiting on approval to order Internet Peering in New Orleans
- LONI connection to LCRP ordered
- LONI connection to LUMCOM ordered
- LONI connection to Grambling ordered
- LONI connection to Nicholls ordered


Long-term Plans:

- Approval from LSU-A to connect to LONI
- Approval from SU-New Orleans to connect to LONI
- Deliver network services to NSU
- Peering with LEARN
- Peering ARE-ON
- Permanent LONI bandwidth to ISB for Dell50T

Issues:

- Unsigned AT&T Local Loop Dark Fiber AUP and CEA
- Unsigned AT&T SURA Fiber Contract
- Missing local loop dark fiber routes especially at La Tech, McNeese and SLU

Planned

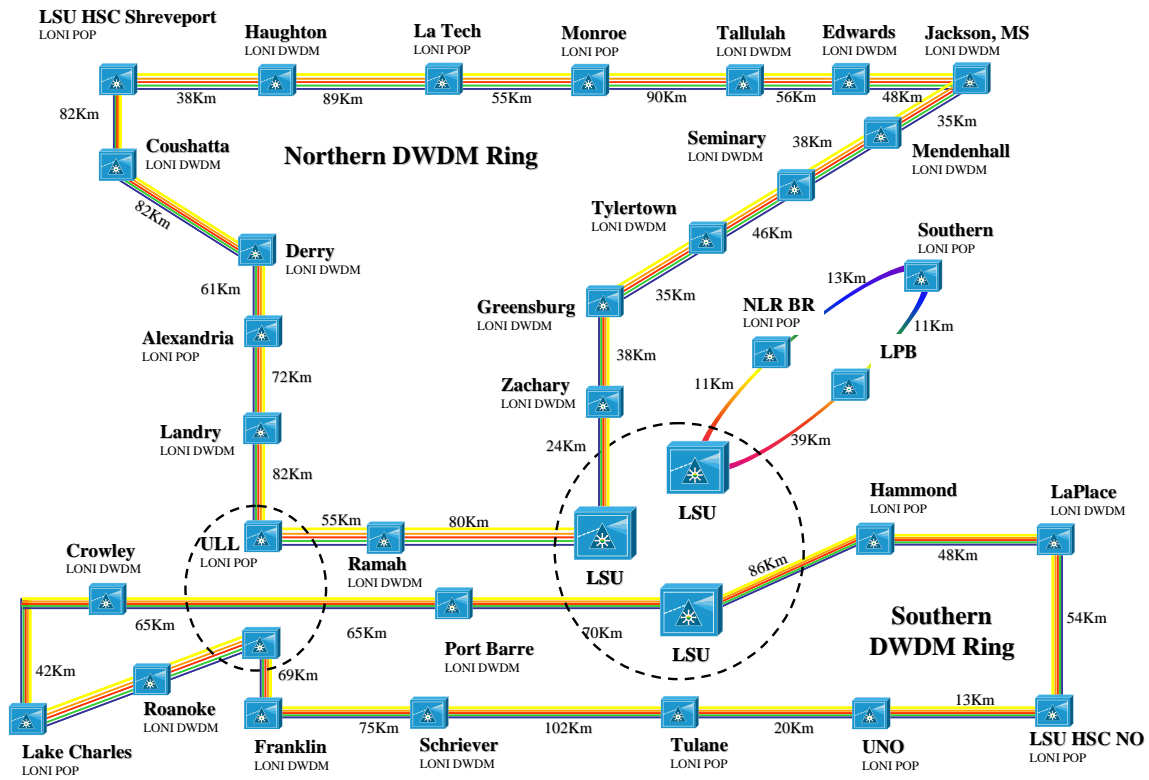

Today

